

BID PROPOSAL FORM BID NO. 2019-002

**BID TO: CITY COMMISSION
CITY OF MARGATE**

1. The undersigned bidder proposes and agrees, if this bid is accepted, to enter into an Agreement with the OWNER in the form included in the Contract Documents to perform the WORK as specified or indicated in said Contract Documents entitled:

CITY OF MARGATE
2018 WATER MAIN IMPROVEMENTS, PHASE II
BID NO. 2019-002

2. Bidder accepts all of the terms and conditions of the Contract Documents, including without limitation those in the "Notice Inviting Bids", and "Instructions to Bidders", dealing with the disposition of the bid security.
3. The bid will remain open for the period stated in the "Notice Inviting Bids", unless otherwise required by law. Bidder will enter into an Agreement within the time and in the manner required in the "Notice Inviting Bids" and the "Instructions to Bidders", and will furnish the insurance certificates, Payment Bond and Performance Bond required by the Contract Documents.
4. It is the Contractor's responsibility to contact the City @ (954) 935-5346 prior to the bid opening to determine if any addenda have been issued on the project. Bidder has examined copies of all the Contract Documents including the following addenda (receipt of all of which is acknowledged):

Number	<u>1</u>	Date	<u>4/16/2019</u>
	<u>2</u>		<u>4/22/2019</u>
	<u>3</u>		<u>4/25/2019</u>

5. Bidder has familiarized itself with the nature and extent of the Contract Documents, WORK, site, locality where the WORK is to be performed, the legal requirements (federal, state and local laws, ordinances, rules and regulations), and the conditions affecting cost, progress or performance of the WORK and has made such independent investigations as bidder deems necessary.
6. This bid is genuine and not made in the interest of or on behalf of any undisclosed person, firm or corporation and is not submitted in conformity with any agreement or rules of any group, association, organization or corporation. Bidder has not directly or indirectly induced or solicited any other bidder to submit a false or sham bid. Bidder has not solicited or induced any person, firm or corporation to refrain from bidding and Bidder has not sought by collusion to obtain for itself any advantage over any other bidder or over Owner.

To all the foregoing, and including all Bid Schedule(s) and information required of bidder contained in this Bid Form, said Bidder further agrees to complete the Work required under the Contract Documents within the Contract Time stipulated in said Contract Documents, and to accept in full payment thereof the Contract Price based on the total bid price(s) named in the aforementioned bidding schedule(s).

BID PROPOSAL FORM BID NO. 2019-002

NAME OF FIRM DBF Construction, LLC

ADDRESS: 1850 NW 15th Avenue, Suite 225, Pompano Beach, FL 33069

NAME OF SIGNER Mark Giannetti
(Print or Type)

TITLE OF SIGNER Vice President

SIGNATURE:  DATE: 5/1/2019

TELEPHONE NO: 954-532-9869 FACSIMILE NO: 954-532-9897

E-MAIL: steph@dbfconst.comcastbiz.net

SCHEDULE OF BID PRICES – BID NO. 2019-002

TO: CITY COMMISSION

CITY OF MARGATE

(Please fill in all blanks and return with your proposal.)

In accordance with your request for proposals and the specifications contained herein, the undersigned proposes the following:

NOTE: BIDDER SHALL PERFORM THE WORK WITH ITS OWN ORGANIZATION, AMOUNTING TO NOT LESS THAN 35 PERCENT OF THE CONTRACT PRICE.

BIDDER AGREES TO PERFORM ALL THE WORK DESCRIBED IN THE CONTRACT DOCUMENTS FOR THE FOLLOWING UNIT PRICES OR LUMP SUMS. BIDS SHALL INCLUDE SALES TAX AND ALL OTHER APPLICABLE TAXES AND BIDDER UNDERSTAND THAT THE EXTENDED TOTAL FOR EACH AND EVERY ITEM IS THE RESULT OF MULTIPLYING THE QUANTITY TIMES THE UNIT COST STATED IN FIGURES. ANY DISCREPANCY BETWEEN THE UNIT AND TOTAL, THE UNIT PREVAILS.

Bid 2019-002 – 2018 Water Main Improvements, Phase II

ITEM NO.	ITEM DESCRIPTION
1	MOBILIZATION & DEMOBILIZATION: The lump sum amount shall include the costs of transporting equipment to and from the site, clean up and disposal of debris, excess pipe, asphalt, surplus excavation, preconstruction investigations/testing, and all other costs incidental or necessary to initiate and terminate construction. The lump sum amount shall also include the preparation of a sediment and erosion control plan (to be submitted to the regulatory agency and City along with the construction permit application), erosion control, temporary construction site fencing (6' chain link), the full cost of providing and maintaining current all performance, payment and maintenance bonds, insurance, and the cost of pulling all required construction permits (City permit fees will be waived). * NOTE: Total line item for mobilization and demobilization cannot exceed 10% of contract. *
2	M.O.T.: Furnish all material, equipment, and labor necessary to provide maintenance of traffic (M.O.T.) including the preparation of the Contractor's proposed maintenance of traffic plan per FDOT and City requirements. The lump sum shall include the cost of barricades, lighting, flagmen, off duty policemen and other work needed to control traffic and minimize inconvenience to the public. * NOTE: Total line item for M.O.T. cannot exceed 5% of contract. *
3	DENSITY TESTING: Density Testing as indicated in Section 01458 And 02315 of the Contract Specifications. * NOTE: Total line item for Density Testing cannot exceed 4% of contract. *

- 4 **STAKEOUT AND AS-BUILTS:** Survey stakeout & certified "As-Built" record drawings. The lump sum amount submitted shall include all the cost of labor, equipment and material necessary to stake out and produce the record drawings for this Lift Station, in accordance with Section 01785 of the Contract Specifications. * NOTE: Total line item for Stakeout/As-Builts cannot exceed 4% of contract. *
- 5 **VIDEOS:** Pre-construction videotapes as indicated in Section 01321 of the Contract Specifications. * NOTE: Total line item for Videos cannot exceed 2% of contract. *

THE PRICE FOR EACH WATER MAIN CONSTRUCTION BID ITEM SHALL INCLUDE, BUT NOT BE LIMITED TO: ALL LABOR, EQUIPMENT AND MATERIALS NECESSARY TO INSTALL AND CONSTRUCT THESE ITEMS IN ACCORDANCE WITH THESE CONTRACT DOCUMENTS WHICH INCLUDE ALL EXCAVATION, RESTORATION, TRENCH SAFETY REQUIREMENTS, EROSION CONTROL, SWPPP/NPDES PERMITTING, SHEETING, DE-WATERING, DE-WATERING PERMITS, PIPE, PIPE RESTRAINTS, CONCRETE THRUST BLOCKS, MAGNETIC DETECTION TAPE, PAINT, CONNECTION TO EXISTING UTILITIES, DEFLECTION TO AVOID EXISTING UTILITIES/TREES, UTILITY/TREE PROTECTION, BEDDING MATERIAL PLACEMENT, BACKFILL MATERIAL PLACEMENT AND COMPACTION, TESTING, INSPECTIONS, SIGNAGE, SIGNALIZATION REPAIR; REMOVAL, PROTECTION, STORAGE AND REINSTALLATION OF PRIVATELY OWNED MAILBOXES, EXISTING SANITARY SEWER REPLACEMENT, DECORATIVE STONE, LANDSCAPING, AND SPRINKLER SYSTEMS EXISTING WITHIN THE WORK ZONE; AND ANY OTHER MISCELLANEOUS WORK. NO ADDITIONAL COMPENSATION SHALL BE MADE FOR CHANGES IN ALIGNMENT OR GRADE TO AVOID EXISTING INFRASTRUCTURE OR FOR ANY DAMAGES BY THE CONTRACTOR BEYOND THE SCOPE OF WORK BEING PERFORMED.

- 6 **ADDITIONAL COMPENSATION FOR EXCAVATION IN HARD ROCK CONDITIONS:** Hard rock conditions are defined as soil types with a Standard Penetration Test N-value greater than 50. Additional compensation for excavation in hard rock will be based upon actual linear feet of pipe installed along hard rock conditions. This bid item shall include, but not be limited to, compensation for Standard Penetration Testing and any additional mobilization, equipment, machinery, well points, crushing, filling, shoring, disposal, labor and all other appurtenances necessary to maintain normal production rates within the limits of hard rock conditions and as define in the specifications.

DIP WATER MAIN INSTALLATIONS (ITEMS 7 – 9): FURNISH ALL MATERIALS, EQUIPMENT AND LABOR NECESSARY FOR THE INSTALLATION OF NEW DUCTILE IRON WATER MAINS. BID ITEMS TO INCLUDE TRENCH RESTORATIONS AND ALL APPURTENANCES NECESSARY.

- 7 **6-INCH DIP WATER MAIN:**
- 8 **8-INCH DIP WATER MAIN:**
- 9 **10-INCH DIP WATER MAIN:**

RESILIENT SEATED GATE VALVE INSTALLATIONS (ITEMS 10 – 12): FURNISH ALL MATERIALS, EQUIPMENT AND LABOR NECESSARY FOR THE INSTALLATION OF NEW GATE VALVES. BID ITEMS TO INCLUDE VALVE BOX RISER, VALVE BOX, CONCRETE COLLAR, IDENTIFICATION MARKER AND ALL OTHER APPURTENANCES NECESSARY.

- 10 **6-INCH RESILIENT SEAT GATE VALVE:**
- 11 **8-INCH RESILIENT SEAT GATE VALVE:**
- 12 **10-INCH RESILIENT SEAT GATE VALVE:**
- 13 **DIP WATER MAIN FITTINGS:** Furnish all materials, equipment, and labor necessary for the installation of new ductile iron fittings. To include all appurtenances necessary.
- 14 **PROPOSED FIRE HYDRANT:** Furnish all materials, equipment, and labor necessary for the installation of proposed or replaced fire hydrants. To include fire hydrant assembly, (1) 6-inch resilient seat gate valve, bollards and all required restraints and DIP spool piece between the valve and hydrant.
- 15 **REMOVE EXISTING FIRE HYDRANT:** Furnish all materials, equipment, and labor necessary to remove the existing tee fitting, gate valve, fire hydrant and all piping between the tee on water main and fire hydrant (all items of value shall be returned to the OWNER). Contractor shall keep existing hydrants in service until the new watermain is certified and placed into service.

CONNECTIONS TO EXISTING ACP WATER MAINS WITH HYMAX COUPLINGS (ITEMS 16 – 18): FURNISH ALL MATERIALS, EQUIPMENT AND LABOR NECESSARY TO MAKE PROPER AND LEGAL CONNECTIONS TO EXISTING **ASBESTOS CEMENT WATER MAINS** PER ALL CURRENT CITY AND PERTAINING GOVERNING REGULATIONS, STANDARDS AND CODES. BID ITEMS TO INCLUDE ALL PERMITS AND APPURTENANCES NECESSARY.

- 16 **6-INCH ACP WATER MAIN CONNECTION W/ 6-INCH HYMAX COUPLING:**
- 17 **8-INCH ACP WATER MAIN CONNECTION W/ 8-INCH HYMAX COUPLING:**
- 18 **10-INCH ACP WATER MAIN CONNECTION WITH 10-INCH HYMAX COUPLING:**
- 19 **REMOVE EXISTING PLUG, CAP OR BLIND FLANGE AND CONNECT TO EXISTING DIP PIPE OR FITTING:** Furnish all materials, equipment, and labor necessary for the connection at existing ductile iron water mains. To include all appurtenances and compliances necessary per current City and pertaining governing regulations, standards and codes.
- 20 **1-INCH BLUE P.E. TUBING WATER SERVICE (SHORT):** Furnish all materials, equipment, and labor necessary for the installation of water service laterals. To include open trench installation/restoration, concrete sidewalk restorations, S.S. double strap tapping saddles, corporation stops, curb stops and all other fittings and appurtenances necessary to make proper connections to existing single or double service meter assembly.

- 21 **1-INCH BLUE P.E. TUBING WATER SERVICE (LONG):** Furnish all materials, equipment, and labor necessary for the installation of water service laterals. To include trenchless installation/restoration, concrete sidewalk restorations, pipe casings, S.S. double strap tapping saddles, corporation stops, curb stops and all other fittings and appurtenances necessary to make proper connections to existing single or double service meter assembly.
- 22 **SINGLE WATER SERVICE METER ASSEMBLY REPLACEMENTS:** Furnish all materials, equipment, and labor necessary for the removal and replacement of existing water service meter assemblies. Bid item to include, but not be limited to, installation of lock wing ball valve, meter (supplied by OWNER), meter box, meter spud, dual check backflow preventer, couplings, connection to service line on private property and all appurtenances necessary to fully replace the existing service assembly. Replacement of water service assemblies shall be handled on a case-by-case basis; quantity shown reflects estimate for ALL meter assemblies encountered on project. CONTRACTOR to coordinate all replacements with OWNER.
- 23 **DOUBLE WATER SERVICE METER ASSEMBLY REPLACEMENTS:** Furnish all materials, equipment, and labor necessary for the removal and replacement of existing water service meter assemblies. Bid item to include, but not be limited to, installation of lock wing ball valve, meter (supplied by OWNER), meter box, meter spud, dual check backflow preventer, couplings, connection to service line on private property and all appurtenances necessary to fully replace the existing service assembly. Existing double service laterals that branch into (2) single meter box assemblies shall be re-installed inside (1) meter box with (2) meters. Replacement of water service assemblies shall be handled on a case-by-case basis; quantity shown reflects estimate for ALL meter assemblies encountered on project. CONTRACTOR to coordinate all replacements with OWNER.
- 24 **TEMPORARY SAMPLE POINT ON WATER MAIN:** Furnish all materials, equipment, and labor necessary for the installation of temporary sample points on water mains. To include all appurtenances and compliances necessary per current City and pertaining governing regulations, standards and codes.
- 25 **TEMPORARY SAMPLE POINT ON FIRE HYDRANT:** Furnish all materials, equipment, and labor necessary for the installation of temporary sample points on fire hydrants. To include all appurtenances and compliances necessary per current City and pertaining governing regulations, standards and codes.
- 26 **DISCONNECT EXISTING 2-INCH GALVANIZED STEEL WATER MAIN:** Furnish all materials, equipment, and labor necessary for the disconnection of existing galvanized steel water mains. To include plugging and sealing existing tap or corporation stop.

GROUT FILL & ABANDON-IN-PLACE EXISTING ACP WATER MAINS (ITEMS 27 – 29): FURNISH ALL MATERIALS, EQUIPMENT AND LABOR NECESSARY FOR THE PROPER AND LEGAL DISCONNECTION, GROUT FILLING AND ABANDONMENT-IN-PLACE OF EXISTING ASBESTOS CEMENT WATER MAINS PER ALL CURRENT CITY AND PERTAINING GOVERNING REGULATIONS, STANDARDS AND CODES. BID ITEMS TO INCLUDE ALL PERMITS AND APPURTENANCES NECESSARY.

- 27 **GROUT FILL AND ABANDON-IN-PLACE EXISTING 6-INCH ACP WATER MAIN:**
- 28 **GROUT FILL AND ABANDON-IN-PLACE EXISTING 8-INCH ACP WATER MAIN:**
- 29 **GROUT FILL AND ABANDON-IN-PLACE EXISTING 10-INCH ACP WATER MAIN:**

REMOVAL OF EXISTING ACP WATER MAINS (ITEMS 30 – 32): FURNISH ALL MATERIALS, EQUIPMENT AND LABOR NECESSARY TO COMPLETE PROPER AND LEGAL REMOVAL OF EXISTING ASBESTOS CEMENT WATER MAINS PER ALL CURRENT CITY AND PERTAINING GOVERNING REGULATIONS, STANDARDS AND CODES. BID ITEMS TO INCLUDE ALL PERMITS AND APPURTENANCES NECESSARY.

- 30 **REMOVAL OF EXISTING 6-INCH ACP WATER MAIN:**
- 31 **REMOVAL OF EXISTING 8-INCH ACP WATER MAIN:**
- 32 **REMOVAL OF EXISTING 10-INCH ACP WATER MAIN:**

PAVEMENT RESTORATIONS (ITEMS 33 – 39): FURNISH ALL MATERIALS, EQUIPMENT AND LABOR NECESSARY FOR THE RESTORATIONS OF EXISTING ASPHALT, CONCRETE AND PAVER/SPECIALTY PAVEMENT DRIVEWAYS, AS WELL AS, ASPHALT PAVEMENT ROADWAYS, CONCRETE SIDEWALKS, ADA APPROVED SIDEWALK RAMPS, ADA APPROVED TRUNCATED DOMES, AND CONCRETE CURB/GUTTER. BID ITEMS TO INCLUDE SAW CUTTING AND REMOVAL OF EXISTING MATERIALS, COMPACTION OF EXISTING BASE MATERIAL, INSTALLATION OF NEW SHELLROCK BASE MATERIAL (AS NECESSARY) AND ALL OTHER APPURTENANCES NECESSARY FOR PROPER RESTORATIONS. TYPICAL RESTORATION LIMITS ARE AS SHOWN ON THE PLANS AND AS DESCRIBED IN THE BID ITEMS BELOW. ACTUAL LIMITS OF RESTORATION SHALL BE DETERMINED IN THE FIELD PER FIELD CONDITIONS AND AS DIRECTED/APPROVED BY THE ENGINEER AND/OR CITY INSPECTOR. THE CONTRACTOR IS RESPONSIBLE FOR ALL DAMAGES OUTSIDE THE RESTORATION LIMITS.

- 33 **ASPHALT DRIVEWAY RESTORATION:** Typical restoration limits shall be between the edge of roadway pavement (or curb/gutter) to right-of-way line (or edge of concrete sidewalk).
- 34 **CONCRETE DRIVEWAY RESTORATION:** Typical restoration limits shall be between the edge of roadway pavement (or curb/gutter) to right-of-way line (or edge of concrete sidewalk).
- 35 **PAVER/SPECIALTY DRIVEWAY RESTORATION:** Typical restoration limits shall be between the edge of roadway pavement (or curb/gutter) to right-of-way line (or edge of concrete sidewalk).

- 36 **ASPHALT ROADWAY RESTORATION:** Shall include milling of existing asphalt pavement outside the trench restoration limits and all required pavements markings to restore roadway to existing conditions or better. The CONTRACTOR shall stay within the restoration limits as per the Construction Plans and will only be paid for the square footage of asphalt within those limits. No additional payment shall be given for temporary asphalt patches or for asphalt areas outside of the defined limits; unless approved by the CITY or ENGINEER prior to conducting the work.
- 37 **CONCRETE SIDEWALK RESTORATION:** Typical removal/restoration limits shall be in full sections (between joints, type "A" or "B" per detail). Concrete sidewalk restoration compensation shall only be given to work associated with water main installation. No compensation will be given for work associated with the installations of service laterals. * NOTE: Costs for sidewalk repairs due to service lateral installations shall be included in Bid Items No. 20 and 21. *
- 38 **CONCRETE CURB RESTORATION:** Typical removal/restoration limits shall be in full sections (between relief/expansion joints).
- 39 **ADA RAMPS & TRUNCATED DOME SIDEWALK PAD:** Furnish all materials, equipment, and labor necessary for the installation of new sidewalk ramps and detectable truncated dome sidewalk pads as per current ADA and FDOT standards and requirements. To include all appurtenances necessary.
- 40 **SOD RESTORATION:** Furnish all materials, equipment, and labor necessary for restoration of sod. To including removal/preparation of existing conditions, installation of top soil, as necessary, and maintenance of restored areas until project completion. The CONTRACTOR shall limit sod damages beyond areas directly related to the work being performed.

TREE REMOVAL AND REPLACEMENT CONTINGENCY: COMPENSATION FOR FOLLOWING CITY ORDINANCES AND ALL PERTAINING GOVERNING REGULATIONS SHALL BE INCLUDED WITH THESE BID ITEMS. CONTINGENCY AMOUNTS SHOWN ARE ESTIMATES AND SHALL BE PAID FOR AS A COST PASS-THROUGH ITEM. PAYMENTS ARE BASED ON ACTUAL COSTS EXPENDED TO PERFORM THE REQUIRED WORK. COSTS SHALL INCLUDE LABOR, MATERIALS AND EQUIPMENT/SERVICES NECESSARY TO REMOVE TREES, STUMPS AND ROOTS WITH PROPER DISPOSAL; TO PURCHASE, TRANSPORT, TRANSPLANT, STAKE, FERTILIZE, WATER AND INSTALL SOIL AMENDMENTS/ROOT BARRIERS WITH THE PROPER MAINTENANCE FOR NEW TREE HEALTH. ACTUAL TREE PLANTING LOCATIONS SHALL BE COORDINATED AND DETERMINED BY THE CITY. REIMBURSABLES ARE BASED ON ACTUAL COSTS. THE OWNER SHALL RECONCILE THE ACTUAL COSTS WITH THE CONTRACTOR AND THE CONTRACTOR SHALL PRODUCE DOCUMENTATION UPON REQUEST VERIFYING ACTUAL COSTS. ONLY COSTS/FEEES SUBSTANTIATED AND APPROVED BY BOTH THE ENGINEER AND OWNER SHALL BE COMPENSATED FOR UNDER THESE BID ITEMS. IF THE AMOUNT IS NOT USED EITHER WHOLLY OR IN PART, THE AMOUNT NOT USED SHALL BE DEDUCTED FROM THE CONTRACT PRICE.

41 **TREE REMOVAL CONTINGENCY:**

42 **TREE REPLACEMENT CONTINGENCY:**

43 **CONTINGENCY:** A contingency for unforeseen equipment, materials, or other work not directly or indirectly included in any of the items listed. All work paid for under this item must be authorized in writing by the ENGINEER and OWNER. If the amount is not used either wholly or in part, the amount not used shall be deducted from the contract price.

ITEM NO.	DESCRIPTION	QTY.	UNIT	UNIT COST	TOTAL COST
1	MOBILIZATION AND DEMOBILIZATION	1	LS	\$90,000.00	\$90,000.00
2	MAINTENANCE OF TRAFFIC	1	LS	\$50,000.00	\$50,000.00
3	DENSITY TESTING	1	LS	\$10,000.00	\$10,000.00
4	STAKEOUT AND AS-BUILT'S	1	LS	\$27,000.00	\$27,000.00
5	VIDEOS	1	LS	\$5,500.00	\$5,500.00
6	ADDITIONAL COMPENSATION FOR EXCAVATION IN HARD ROCK CONDITIONS	2,500	LF	\$1.80	\$4,500.00
7	6-INCH DIP WATER MAIN INSTALLATIONS	11,366	LF	\$38.54	\$438,045.64
8	8-INCH DIP WATER MAIN INSTALLATIONS	540	LF	\$41.51	\$22,416.17
9	10-INCH DIP WATER MAIN INSTALLATIONS	154	LF	\$49.02	\$7,549.30
10	6-INCH RESILIENT SEAT GATE VALVE	42	EA	\$1,021.04	\$42,883.68
11	8-INCH RESILIENT SEAT GATE VALVE	4	EA	\$1,424.37	\$5,697.48
12	10-INCH RESILIENT SEAT GATE VALVE	3	EA	\$1,970.80	\$5,912.40
13	DIP WATER MAIN FITTINGS	3.2	TN	\$6,428.40	\$20,570.88
14	PROPOSED FIRE HYDRANT	32	EA	\$4,580.84	\$146,586.88
15	REMOVE EXISTING FIRE HYDRANT	12	EA	\$454.94	\$5,459.28
16	6-INCH ACP WATER MAIN CONNECTION WITH 6-INCH HYMAX COUPLING	33	EA	\$1,383.20	\$45,645.60
17	8-INCH ACP WATER MAIN CONNECTION WITH 8-INCH HYMAX COUPLING	5	EA	\$1,430.90	\$7,154.50
18	10-INCH ACP WATER MAIN CONNECTION WITH 10-INCH HYMAX COUPLING	5	EA	\$1,489.20	\$7,446.00
19	REMOVE EXISTING PLUG, CAP OR BLIND FLANGE AND CONNECT TO EXISTING DIP PIPE OR FITTING	4	EA	\$1,132.54	\$4,530.16
20	1-INCH BLUE P.E. TUBING WATER SERVICE (SHORT)	72	EA	\$316.99	\$22,823.28
21	1-INCH BLUE P.E. TUBING WATER SERVICE (LONG)	69	EA	\$973.23	\$67,152.87
22	SINGLE WATER SERVICE METER ASSEMBLY REPLACEMENTS	25	EA	\$613.97	\$15,349.25
23	DOUBLE WATER SERVICE METER ASSEMBLY REPLACEMENTS	116	EA	\$764.77	\$88,713.32
24	TEMPORARY SAMPLE POINT ON WATER MAIN	14	EA	\$486.03	\$6,804.42
25	TEMPORARY SAMPLE POINT ON FIRE HYDRANT	18	EA	\$261.32	\$4,703.76
26	DISCONNECT EXISTING 2-INCH GALVANIZED STEEL WATER MAIN	3	EA	\$572.50	\$1,717.50
27	GROUT FILL AND ABANDON-IN-PLACE EXISTING 6-INCH ACP WATER MAIN	1,404	LF	\$4.17	\$5,854.68
28	GROUT FILL AND ABANDON-IN-PLACE EXISTING 8-INCH ACP WATER MAIN	414	LF	\$2.33	\$964.62
29	GROUT FILL AND ABANDON-IN-PLACE EXISTING 10-INCH ACP WATER MAIN	68	LF	\$3.79	\$257.72
30	REMOVAL OF EXISTING 6-INCH ACP WATER MAIN	682	LF	\$11.00	\$7,502.00
31	REMOVAL OF EXISTING 8-INCH ACP WATER MAIN	88	LF	\$11.00	\$968.00
32	REMOVAL OF EXISTING 10-INCH ACP WATER MAIN	88	LF	\$13.25	\$1,166.00
33	ASPHALT DRIVEWAY RESTORATION	1,953	SY	\$32.10	\$62,687.05
34	CONCRETE DRIVEWAY RESTORATION	995	SY	\$27.50	\$27,362.50
35	PAVER/SPECIALTY DRIVEWAY RESTORATION	244	SY	\$38.44	\$9,380.00
36	ASPHALT ROADWAY RESTORATION	2,270	SY	\$43.00	\$97,610.00
37	CONCRETE SIDEWALK RESTORATION	241	SY	\$22.16	\$5,340.56
38	CONCRETE CURB RESTORATION	495	LF	\$46.00	\$22,770.00
39	ADA RAMPS AND TRUNCATED DOME SIDEWALK PAD	22	EA	\$1,300.00	\$28,600.00

40	SOD RESTORATION	14,812	SY	\$9.63	\$142,565.50
41	TREE REMOVAL CONTINGENCY	1	AL	\$37,000.00	\$37,000.00
42	TREE REPLACEMENT CONTINGENCY	1	AL	\$50,000.00	\$50,000.00

Note: City permit fees shall not be waived and should be included in your bid proposal.

DESCRIPTION	TOTAL COST
TOTAL BASE BID AMOUNT (ITEMS 1 – 42)	\$ <u>1,654,191.01</u>
CONTINGENCY (ITEM 43)	\$ 90,000.00
COST OF INDEMNIFICATION	\$ 100.00
GRAND TOTAL FOR ALL ITEMS	\$ <u>1,744,291.01</u>

ALL BIDS MUST BE SIGNED WITH THE VENDOR NAME AND BY AN OFFICER OR EMPLOYEE HAVING THE AUTHORITY TO BIND THE COMPANY OR FIRM BY SIGNATURE.

REQUIRED PHASING PLAN ENCLOSED? YES ✓ NO

MATERIAL SAFETY DATA SHEETS ENCLOSED? N/A YES NO

SPECIFICATION SHEETS/BROCHURES? YES ✓ NO

WILL YOUR FIRM ACCEPT PAYMENT VIA A CITY OF MARGATE VISA CARD? YES ✓ NO

HAVE YOUR INSURANCE REPRESENTATIVE REVIEW THE SAMPLE INSURANCE CERTIFICATE TO ENSURE COMPLIANCE.

BIDDER'S GENERAL INFORMATION:

The bidder shall furnish the following information. Additional sheets shall be attached as required. Failure to complete Item Nos. 1, 3, and 8 will cause the bid to be non-responsive and may cause its rejection. In any event, no award will be made until all of the Bidder's General Information (i.e., items 1 through 9 inclusive) is delivered to the OWNER.

- (1) Contractor's name and address:
DBF Construction, LLC
1850 NW 15th Avenue, Suite 225
Pompano Beach, FL 33069
- (2) Contractor's telephone number: 954-532-9869
- (3) Contractor's license: Primary classification General Contractor / Underground Utility
State License Number CGC1512467 / CUC1224328
Supplemental classifications held, if any: _____
Name of Licensee, if different from (1) above: Ilia Lyssenko

- (4) Name of person who inspected site of proposed WORK for your firm:

Name: Mark Giannetti Date of Inspection: 4/9/2019
- (5) Name, address, and telephone number of surety company and agent who will provide the required bonds on this contract: Surety: The Guarantee Company of North America USA
Surety Address: One Towne Square, Suite 1470, South Field, MI 48076; Surety Phone: 248-281-0281
Agent: Zervos Group, Inc., Address: 24724 Farmbrook Rd., Southfield, MI 48034, P: 248-663-5395
- (6) Attach to this bid, the experience resume of the person who will be designated chief construction superintendent or on site construction manager.
- (7) Attach to this bid a financial statement, references, and other information, sufficiently comprehensive to permit an appraisal of Contractor's current financial condition.

(8) List 3 projects completed as of recent date involving work of similar type and complexity:

PROJECT NAME	CONTRACT PRICE	NAME, ADDRESS AND TELEPHONE NUMBER OF OWNER
Bid Pack 11	\$2,664,548.12	Owner: City of Oakland Park
		C: Jim Moore P: 954-630-4432
		Address: 5100 NE 12th Terrace
		Oakland Park, FL 33334
Reuse System Phase I	\$1,752,252.39	Owner: City of Pompano Beach
		C: Tammy Good P: 954-650-7783
		Address: 1201 NE 5th Ave.
		Pompano Beach, FL 33060
South County Water Services Replacement Phase 5	\$2,065,681.87	O: Palm Beach County
		C: Joseph Tanacredi P: 561-493-6088
		Address: 8100 Forest Hill Blvd.
		West Palm Beach, FL 33413

(9) Subcontractors: The bidder further proposes that as part of their submittal, attached is a list of subcontracting firms or businesses that will be awarded subcontracts for portions of the work in the event the bidder is awarded the Contract: True Haul Trucking, Compass Point Surveyors

BID BOND

KNOW ALL MEN BY THESE PRESENTS:

That we DBF Construction, LLC as Principal, and The Guarantee Company of North America USA as Surety, are held and firmly bound unto City of Margate, hereinafter called "City" in the sum of (\$ (5%)) FIVE PERCENT OF BID AMOUNT dollars, (not less than 5 percent of the total amount of the bid) for the payment of which sum, well and truly to be made, we bind ourselves, our heirs, executors, administrators, successors, and assigns, jointly and severally, firmly by these presents.

WHEREAS, said Principal has submitted a bid to said City to perform the Work required under the bidding schedule of the City's Contract Documents entitled:

CITY OF MARGATE
BID NO. 2019-002
2018 WATER MAIN IMPROVEMENTS, PHASE II

NOW THEREFORE, if said Principal is awarded a contract by said City and, within the time and in the manner required in the "Notice Inviting Bids" and the "Instructions to Bidders" enters into a written Agreement on the form of the agreement bound with said Contract Documents, furnishes the required certificates of insurance, and furnishes the required Performance Bond, then this obligation shall be null and void, otherwise it shall remain in full force and effect. In the event suit is brought upon this bond by said City and City prevails, said Surety shall pay all costs incurred by said City in such suit, including a reasonable attorney's fee to be fixed by the court.

SIGNED AND SEALED, this 23rd day of April, 2019

DBF Construction, LLC

(Principal)

By: 

(SIGNATURE) Mark Gignetti V.P

The Guarantee Company of North America USA

(Surety)

By: 

(SIGNATURE) Angelo G. Zervos, Attorney-in-Fact

STATE OF FLORIDA, COUNTY OF BROWARD: BEFORE ME PERSONALLY APPEARED THE ABOVE TO ME WELL KNOWN AND KNOWN TO ME TO BE THE PERSONS DESCRIBED IN AND WHO EXECUTED THE FOREGOING INSTRUMENT, AND ACKNOWLEDGED TO AND BEFORE ME THAT THEY EXECUTED SAID INSTRUMENT FOR THE PURPOSES THEREIN EXPRESSED.

WITNESS MY HAND AND OFFICIAL SEAL, THIS 23 DAY OF April, 2019

NOTARY PUBLIC: 





The Guarantee Company of North America USA
Southfield, Michigan

POWER OF ATTORNEY

NOW ALL BY THESE PRESENTS: That **THE GUARANTEE COMPANY OF NORTH AMERICA USA**, a corporation organized and existing under the laws of the State of Michigan, having its principal office in Southfield, Michigan, does hereby constitute and appoint

Gus E. Zervos, Angelo G. Zervos, David C. Lange, Donald W. Burden, Stephen M. Zervos, Michael G. Zervos
Zervos Group, Inc.

its true and lawful attorney(s)-in-fact to execute, seal and deliver for and on its behalf as surety, any and all bonds and undertakings, contracts of indemnity and other writings obligatory in the nature thereof, which are or may be allowed, required or permitted by law, statute, rule, regulation, contract or otherwise.

The execution of such instrument(s) in pursuance of these presents, shall be as binding upon **THE GUARANTEE COMPANY OF NORTH AMERICA USA** as fully and amply, to all intents and purposes, as if the same had been duly executed and acknowledged by its regularly elected officers at the principal office.

The Power of Attorney is executed and may be certified so, and may be revoked, pursuant to and by authority of Article IX, Section 9.03 of the By-Laws adopted by the Board of Directors of **THE GUARANTEE COMPANY OF NORTH AMERICA USA** at a meeting held on the 31st day of December, 2003. The President, or any Vice President, acting with any Secretary or Assistant Secretary, shall have power and authority:

1. To appoint Attorney(s)-in-fact, and to authorize them to execute on behalf of the Company, and attach the Seal of the Company thereto, bonds and undertakings, contracts of indemnity and other writings obligatory in the nature thereof; and
2. To revoke, at any time, any such Attorney-in-fact and revoke the authority given, except as provided below
3. In connection with obligations in favor of the Florida Department of Transportation only, it is agreed that the power and authority hereby given to the Attorney-in-Fact includes any and all consents for the release of retained percentages and/or final estimates on engineering and construction contracts required by the State of Florida Department of Transportation. It is fully understood that consenting to the State of Florida Department of Transportation making payment of the final estimate to the Contractor and/or its assignee, shall not relieve this surety company of any of its obligations under its bond.
4. In connection with obligations in favor of the Kentucky Department of Highways only, it is agreed that the power and authority hereby given to the Attorney-in-Fact cannot be modified or revoked unless prior written personal notice of such intent has been given to the Commissioner – Department of Highways of the Commonwealth of Kentucky at least thirty (30) days prior to the modification or revocation.

Further, this Power of Attorney is signed and sealed by facsimile pursuant to resolution of the Board of Directors of the Company adopted at a meeting duly called and held on the 6th day of December 2011, of which the following is a true excerpt:

RESOLVED that the signature of any authorized officer and the seal of the Company may be affixed by facsimile to any Power of Attorney or certification thereof authorizing the execution and delivery of any bond, undertaking, contracts of indemnity and other writings obligatory in the nature thereof, and such signature and seal when so used shall have the same force and effect as though manually affixed.

IN WITNESS WHEREOF, **THE GUARANTEE COMPANY OF NORTH AMERICA USA** has caused this instrument to be signed and its corporate seal to be affixed by its authorized officer, this 1st day of March, 2018.



THE GUARANTEE COMPANY OF NORTH AMERICA USA

Stephen C. Ruschak, President & Chief Operating Officer

Randall Musselman, Secretary

STATE OF MICHIGAN
County of Oakland

On this 1st day of March, 2018 before me came the individuals who executed the preceding instrument, to me personally known, and being by me duly sworn, said that each is the herein described and authorized officer of The Guarantee Company of North America USA; that the seal affixed to said instrument is the Corporate Seal of said Company; that the Corporate Seal and each signature were duly affixed by order of the Board of Directors of said Company.



Cynthia A. Takai
Notary Public, State of Michigan
County of Oakland
My Commission Expires February 27, 2024
Acting in Oakland County

IN WITNESS WHEREOF, I have hereunto set my hand at The Guarantee Company of North America USA offices the day and year above written.

I, Randall Musselman, Secretary of **THE GUARANTEE COMPANY OF NORTH AMERICA USA**, do hereby certify that the above and foregoing is a true and correct copy of a Power of Attorney executed by **THE GUARANTEE COMPANY OF NORTH AMERICA USA**, which is still in full force and effect.



IN WITNESS WHEREOF, I have thereunto set my hand and attached the seal of said Company this 23rd day of April, 2019

Randall Musselman, Secretary

REFERENCE SHEET

In order to receive Bid Award consideration on the proposed bid, it is a mandatory requirement that the following "Information Sheet" must be completed and returned with your bid. This information may be used in determining the Bid Award for this contract.

BIDDER (COMPANY NAME): DBF Construction, LLC

ADDRESS: 1850 NW 15th Avenue, Suite 225, Pompano Beach, FL 33069 TELEPHONE NO: 954-532-9869

CONTACT PERSON: Mark Giannetti TITLE: Vice President

NUMBER OF YEARS IN BUSINESS: 13

ADDRESS OF NEAREST FACILITY: 1850 NW 15th Avenue, Suite 225, Pompano Beach, FL 33069

LIST THREE (3) COMPANIES OR GOVERNMENTAL AGENCIES WHERE THESE PRODUCTS AND SERVICES HAVE BEEN PROVIDED IN THE LAST YEAR.

1. Company Name: City of Oakland Park

Address: 5100 NE 12th Terrace, Oakland Park, FL 33334

Contact Person: Jim Moore Title: Construction Manager

Phone: 954-630-4432

2. Company Name: City of Pompano Beach

Address: 1201 NE 5th Avenue, Pompano Beach, FL 33060

Contact Person: Tammy Good Title: Engineering Project Manager III

Phone: 954-786-5512

3. Company Name: Palm Beach County

Address: 8100 Forest Hill Blvd., West Palm Beach, FL 33413

Contact Person: Joseph Tanacredi Title: Project Manager

Phone: 561-493-6088

BID NO: 2019-002



NON-COLLUSIVE AFFIDAVIT FOR

Bid No. 2019-002 – 2018 Water Main Improvements – Phase II

State of Florida)

County of Broward)

Mark Giannetti

_____ being first duly sworn, deposes
and says that:

He/she is the Owner, (Owner, Partner, Officer, Representative or Agent) of DBF Construction, LLC, the Offeror that has submitted the attached Proposal;

He/she is fully informed regarding the preparation and contents of the attached Proposal and of all pertinent circumstances regarding such Proposal;

Such Proposal is genuine and is not a collusive or sham Proposal;

Neither the said Offeror nor any of its officers, partners, owners, agents, representatives, employees or parties in interest, including this affiant, have in any way colluded, conspired, connived or agreed, directly or indirectly, with any other Offeror, firm, or person to submit a collusive or sham Proposal in connection with the Work for which the attached Proposal has been submitted; or to refrain from bidding in connection with such Work; or have in any manner, directly or indirectly, sought by agreement or collusion, or communication, or conference with any Offeror, firm, or person to fix the price or prices in the attached Proposal or of any other Offeror, or to fix any overhead, profit, or cost elements of the Proposal price or the Proposal price of any other Offeror, or to secure through any collusion, conspiracy, connivance, or unlawful agreement any advantage against (Recipient), or any person interested in the proposed Work;

The price or prices quoted in the attached Proposal are fair and proper and are not tainted by any collusion, conspiracy, connivance, or unlawful agreement on the part of the Offeror or any other of its agents, representatives, owners, employees or parties in interest, including this affiant.

Signed, sealed and delivered in the presence of:

Witness _____

Witness _____

By _____

Mark Giannetti

Printed Name

Vice President

Title

ACKNOWLEDGMENT
NON-COLLUSIVE AFFIDAVIT FOR
Bid No. 2019-002 – 2018 Water Main Improvements – Phase II

State of Florida
County of Broward

On this the 1 day of May, 2018, before me, the undersigned Notary Public of the State of Florida, personally appeared

Mark Giannetti and
(Name(s) of individual(s) who appeared before notary)

whose name(s) is/are Subscribed to within the instrument, and he/she/they acknowledge that he/she/they executed it.

WITNESS my hand
and official seal.

NOTARY PUBLIC
SEAL OF OFFICE:




NOTARY PUBLIC, STATE OF FLORIDA

Stephany Campo

(Name of Notary Public: Print,
Stamp, or Type as Commissioned)

☒ Personally known to me, or
☐ Produced identification:

(Type of Identification Produced)

☒ DID take an oath, or ☐ DID NOT take an oath

DRUG-FREE WORKPLACE PROGRAM FORM

In accordance with Section 287.087, State of Florida Statutes, preference shall be given to businesses with Drug-free Workplace Programs. Whenever two or more bids which are equal with respect to price, quality and service are received for the procurement of commodities or contractual service, a bid received from a business that certifies that it has implemented a Drug-free Workplace Program shall be given preference in the award process. In the event that none of the tied vendors have a Drug-free Workplace program in effect the City reserves the right to make final Decisions in the City's best interest. In order to have a Drug-free Workplace Program, a business shall:

1. Publish a statement notifying employees that the unlawful manufacture, distribution, dispensing, possession, or use of a controlled substance is prohibited in the workplace and specifying the actions that will be taken against employees for violations of such prohibition.
2. Inform employees about the dangers of drug abuse in the workplace, the business's policy of maintaining a drug-free workplace, any available drug counseling, rehabilitation, and employee assistance programs, and the penalties that may be imposed upon employees for drug abuse violations.
3. Give each employee engaged in providing the commodities or contractual services that are under bid a copy of the statement specified in subsection (1).
4. In the statement specified in subsection (1), notify employees that, as a condition of working on the commodities or contractual services that are under bid, the employee will abide by the terms of the statement and will notify the employer of any conviction of, or plea of guilty or nolo contendere to, any violation of Chapter 893 or of any controlled substance law of the United States or any State, for a violation occurring in the workplace no later than five (5) days after such conviction.
5. Impose a sanction on, or require the satisfactory participation in a drug abuse assistance or rehabilitation program if such is available in the employee's community by any employee who is convicted.
6. Make a good faith effort to continue to maintain a drug-free workplace through implementation.

If bidder's company has a Drug-free Workplace Program, so certify below:

AS THE PERSON AUTHORIZED TO SIGN THE STATEMENT, I CERTIFY THAT THIS FIRM COMPLIES FULLY WITH THE ABOVE REQUIREMENTS.

SIGNATURE OF BIDDER: 

DATE: 5/1/2019

BID NO: 2019-002

COMPLIANCE WITH OCCUPATIONAL SAFETY AND HEALTH ACT

Bidder certifies that all material, equipment, etc. contained in this bid meets all O.S.H.A. requirements. Bidder further certifies that if he/she is the successful bidder, and the material, equipment, etc., delivered is subsequently found to be deficient in any O.S.H.A. requirement in effect on date of delivery, all costs necessary to bring the material, equipment, etc. into compliance with the aforementioned requirements shall be borne by the bidder.

OCCUPATIONAL HEALTH AND SAFETY DATA SHEET REQUIRED:

In compliance with Chapter 442, Florida Statutes, any item delivered from a contract resulting from this bid must be accompanied by a SAFETY DATA SHEET (SDS). The SDS must include the following information:

- A. The chemical name and the common name of the toxic substance.
- B. The hazards or other risks in the use of the toxic substances, including:
 - 1. The potential for fire, explosion, corrosivity and reactivity;
 - 2. the known acute and chronic health effects of risks from exposure, including the medical conditions which are generally recognized as being aggravated by exposure to the toxic substance; and
 - 3. the primary routes of entry and symptoms of overexposure.
- C. The proper precautions, handling practices, necessary personal protective equipment, and other safety precautions in the use of or exposure to the toxic substances, including appropriate emergency treatment in case of overexposure.
- D. The emergency procedure for spills, fire, disposal, and first aid.
- E. A description in lay terms of the known specific potential health risks posed by the toxic substances intended to alert any person reading this information.
- F. The year and month, if available, that the information was compiled and the name, address and emergency telephone number of the manufacturer responsible for preparing the information.

BID NO: 2019-002

ACKNOWLEDGEMENT FORM

ADDENDUM NO. 1

BID NO. 2019-002

2018 WATER MAIN IMPROVEMENTS - PHASE II


I acknowledge receipt of Addendum No. 1 for BID No. 2019-002, Water Main Improvements - Phase II. This addendum contains eleven (11) pages. Please include the original of this form in your qualifications submission.

Company

Name: DBF Construction, LLC

Address: 1850 NW 15th Avenue, Suite 225, Pompano Beach, FL 33069

Name of
Signer Mark Giannetti
(please print)

Signature: 

Date: 4/16/2019

Telephone: 954-532-9869

Facsimile: 954-532-9897

Please fax your completed form to (954) 935-5258 or e-mail to purchase@margatefl.com.

Spencer L. Shambray

Spencer Shambray, CPPB
Purchasing Manager

Tuesday, April 16, 2019

NOTE: The original of this form must be included with your qualifications submission.

ACKNOWLEDGEMENT FORM

ADDENDUM NO. 2

BID NO. 2019-002

2018 WATER MAIN IMPROVEMENTS - PHASE II


I acknowledge receipt of Addendum No. 2 for BID No. 2019-002, Water Main Improvements - Phase II. This addendum contains two (2) pages. Please include the original of this form in your qualifications submission.

Company

Name: DBF Construction, LLC

Address: 1850 NW 15th Avenue, Suite 225, Pompano Beach, FL 33069

Name of Signer Mark Giannetti
(please print)

Signature: 

Date: 4/23/2019

Telephone: 954-532-9869

Facsimile: 954-532-9897

Please fax your completed form to (954) 935-5258 or e-mail to purchase@margatefl.com.

Spencer Shambray

Spencer Shambray, CPPB
Purchasing Manager

Monday, April 22, 2019

NOTE: The original of this form must be included with your qualifications submission.

ACKNOWLEDGEMENT FORM

ADDENDUM NO. 3

BID NO. 2019-002

2018 WATER MAIN IMPROVEMENTS - PHASE II

I acknowledge receipt of Addendum No. 3 for BID No. 2019-002, Water Main Improvements - Phase II. This addendum contains three (3) pages. Please include the original of this form in your qualifications submission.

Company

Name: DBF Construction, LLC

Address: 1850 NW 15th Avenue, Suite 225, Pompano Beach, FL 33069

Name of

Signer Mark Giannetti

(please print)

Signature: 

Date: 4/26/2019

Telephone: 954-532-9869

Facsimile: 954-532-9897

Please fax your completed form to (954) 935-5258 or e-mail to purchase@margatefl.com.


Spencer L. Shambray

Spencer Shambray, CPPB
Purchasing Manager

Thursday, April 25, 2019

NOTE: The original of this form must be included with your qualifications submission.

Phasing plan & Construction Schedule

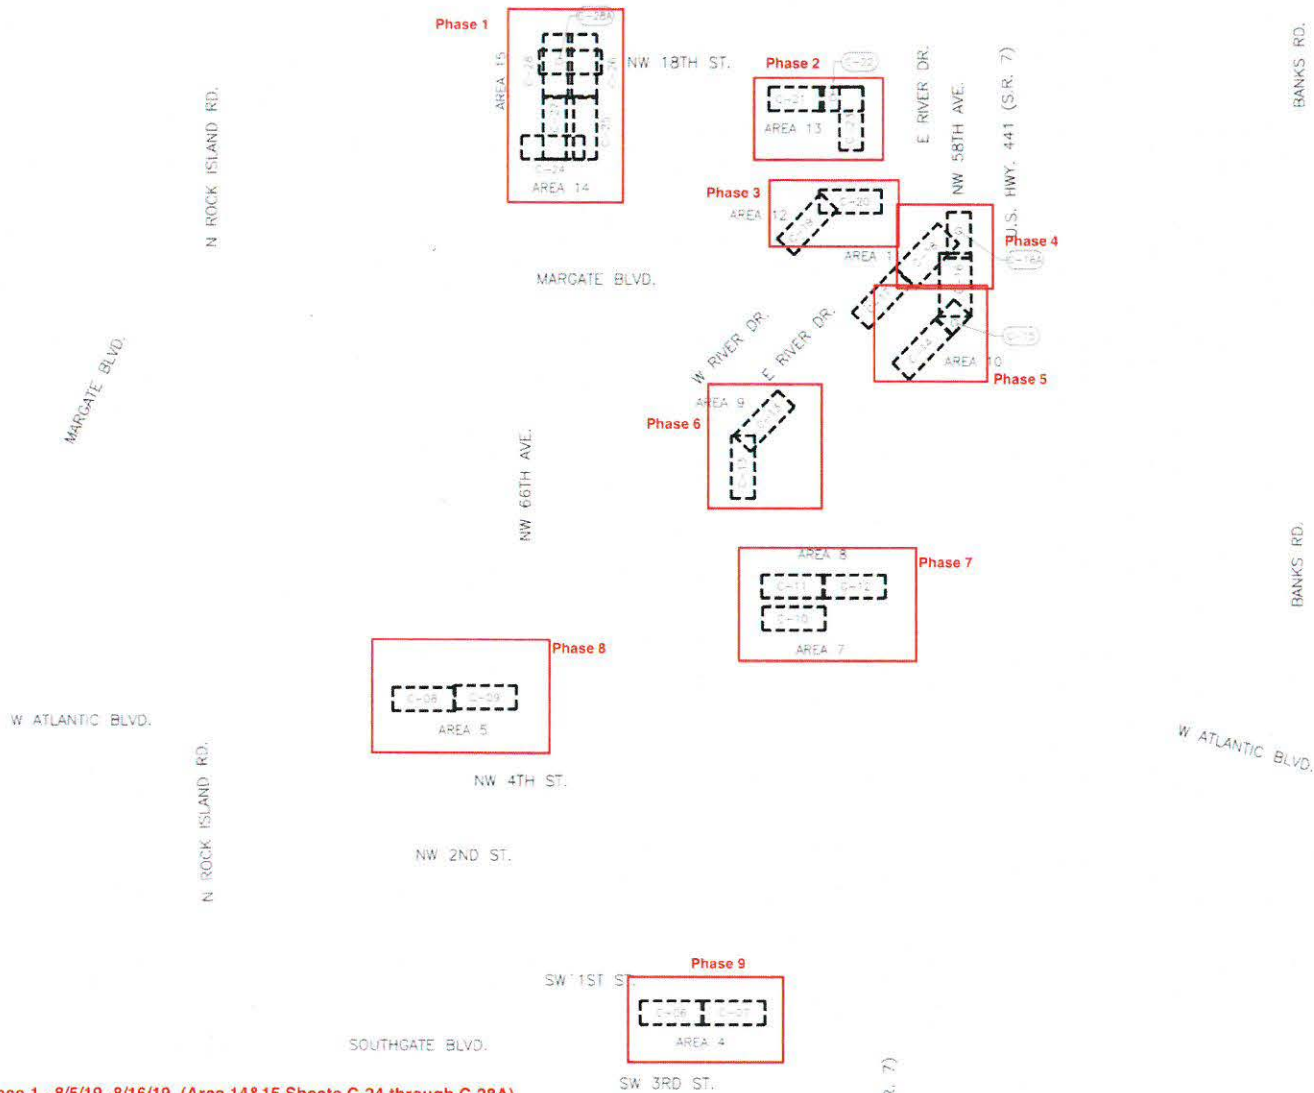

Phase 1 - 8/5/19 - 8/16/19 (Area 14&15 Sheets C-24 through C-28A)

Phase 2 - 8/19/19 - 8/30/19 (Area 13 Sheets C-21 through C-23)

Phase 3 - 9/3/19 - 9/16/19 (Area 12 Sheets C-19 through C-20)

Phase 4 - 9/17/19 - 9/30/19 (Area 11 Sheets C-16, C-16A, C-18)

Phase 5 - 10/1/19 - 10/14/19 (Area 10 Sheet C-14, C-15, C-17)

Phase 6 - 10/15/19 - 10/28/19 (Area 9 Sheet C-13)

Phase 7 - 10/29/19 - 11/11/19 (Area 8 Sheet C-10 through C-12)







Phase 8 - 11/12/19 - 11/25/19 (Area 5 Sheet C-8 through C-9)















Phase 9 - 11/26/19 - 12/10/19 (Area 4 Sheet C-6 through C-7)















Phase 10 - 12/11/19 - 12/26/19 (Area 1 Sheet C-1 through C-2)

Phase 11 - 12/27/19 - 1/13/19 (Area 2&3 Sheet C-3 through C-5)

Phases shall be completed in numerical order with 2 crews working on each phase simultaneously. As Crew 1 installs Pipe Crew 2 follows to install services as well as restoration.

















ID		Task Mode	Task Name	Duration	Start	Finish	% Complete	Mar 17, '19													
								W	T	F	S	S	M	T	W	T					
1			Pre Construction Meeting	1 day	Mon 7/29/19	Mon 7/29/19	0%														
2			Pre Construction Video	2 days	Mon 7/22/19	Tue 7/23/19	0%														
3			Notice to Proceed	1 day	Mon 7/29/19	Mon 7/29/19	0%														
4			Submission of Shop Drawings	6 days	Mon 7/22/19	Mon 7/29/19	0%														
5			Approval of Shop Drawings	6 days	Mon 7/22/19	Mon 7/29/19	0%														
6			Placement of equipment & Material orders	12 days	Mon 7/22/19	Tue 8/6/19	0%														
7			Delivery of equipment and material Orders	15 days	Tue 7/23/19	Mon 8/12/19	0%														
8			Mobilization	2 days	Thu 8/1/19	Fri 8/2/19	0%														
9							0%														
10			Pipe Installation	111 days	Mon 8/5/19	Mon 1/13/20	0%														
11			Phase 1 Crew 1 - Pipe Installation	10 days	Mon 8/5/19	Fri 8/16/19	0%														
12			Phase 1 Crew 2 - Services & Restoration	10 days	Mon 8/5/19	Fri 8/16/19	0%														
13			Phase 2 Crew 1 - Pipe Installation	10 days	Mon 8/19/19	Fri 8/30/19	0%														
14			Phase 2 Crew 2 - Services & Restoration	10 days	Mon 8/19/19	Fri 8/30/19	0%														
15			Phase 3 Crew 1 - Pipe Installation	10 days	Tue 9/3/19	Mon 9/16/19	0%														
16			Phase 3 Crew 2 - Services & Restoration	10 days	Tue 9/3/19	Mon 9/16/19	0%														


Project: Margate Watermain Ph Date: Tue 4/30/19	Task		Inactive Summary		External Tasks
	Split		Manual Task		External Milestone
	Milestone		Duration-only		Deadline
	Summary		Manual Summary Rollup		Progress
	Project Summary		Manual Summary		Manual Progress
	Inactive Task		Start-only		
	Inactive Milestone		Finish-only		
Page 1					

ID		Task Mode	Task Name	Duration	Start	Finish	% Complete	Mar 17, '19													
								W	T	F	S	S	M	T	W	T					
17			Phase 4 Crew 1 - Pipe Installation	10 days	Tue 9/17/19	Mon 9/30/19	0%														
18			Phase 4 Crew 2 - Services & Restoration	10 days	Tue 9/17/19	Mon 9/30/19	0%														
19			Phase 5 Crew 1 - Pipe Installation	10 days	Tue 10/1/19	Mon 10/14/19	0%														
20			Phase 5 Crew 2 - Services & Restoration	10 days	Tue 10/1/19	Mon 10/14/19	0%														
21			Phase 6 Crew 1 - Pipe Installation	10 days	Tue 10/15/19	Mon 10/28/19	0%														
22			Phase 6 Crew 2 - Services & Restoration	10 days	Tue 10/15/19	Mon 10/28/19	0%														
23			Phase 7 Crew 1 - Pipe Installation	10 days	Tue 10/29/19	Mon 11/11/19	0%														
24			Phase 7 Crew 2 - Services & Restoration	10 days	Tue 10/29/19	Mon 11/11/19	0%														
25			Phase 8 Crew 1 - Pipe Installation	10 days	Tue 11/12/19	Mon 11/25/19	0%														
26			Phase 8 Crew 2 - Services & Restoration	10 days	Tue 11/12/19	Mon 11/25/19	0%														
27			Phase 9 Crew 1 - Pipe Installation	10 days	Tue 11/26/19	Tue 12/10/19	0%														
28			Phase 9 Crew 2 - Services & Restoration	10 days	Tue 11/26/19	Tue 12/10/19	0%														
29			Phase 10 Crew 1 - Pipe Installation	10 days	Wed 12/11/19	Thu 12/26/19	0%														







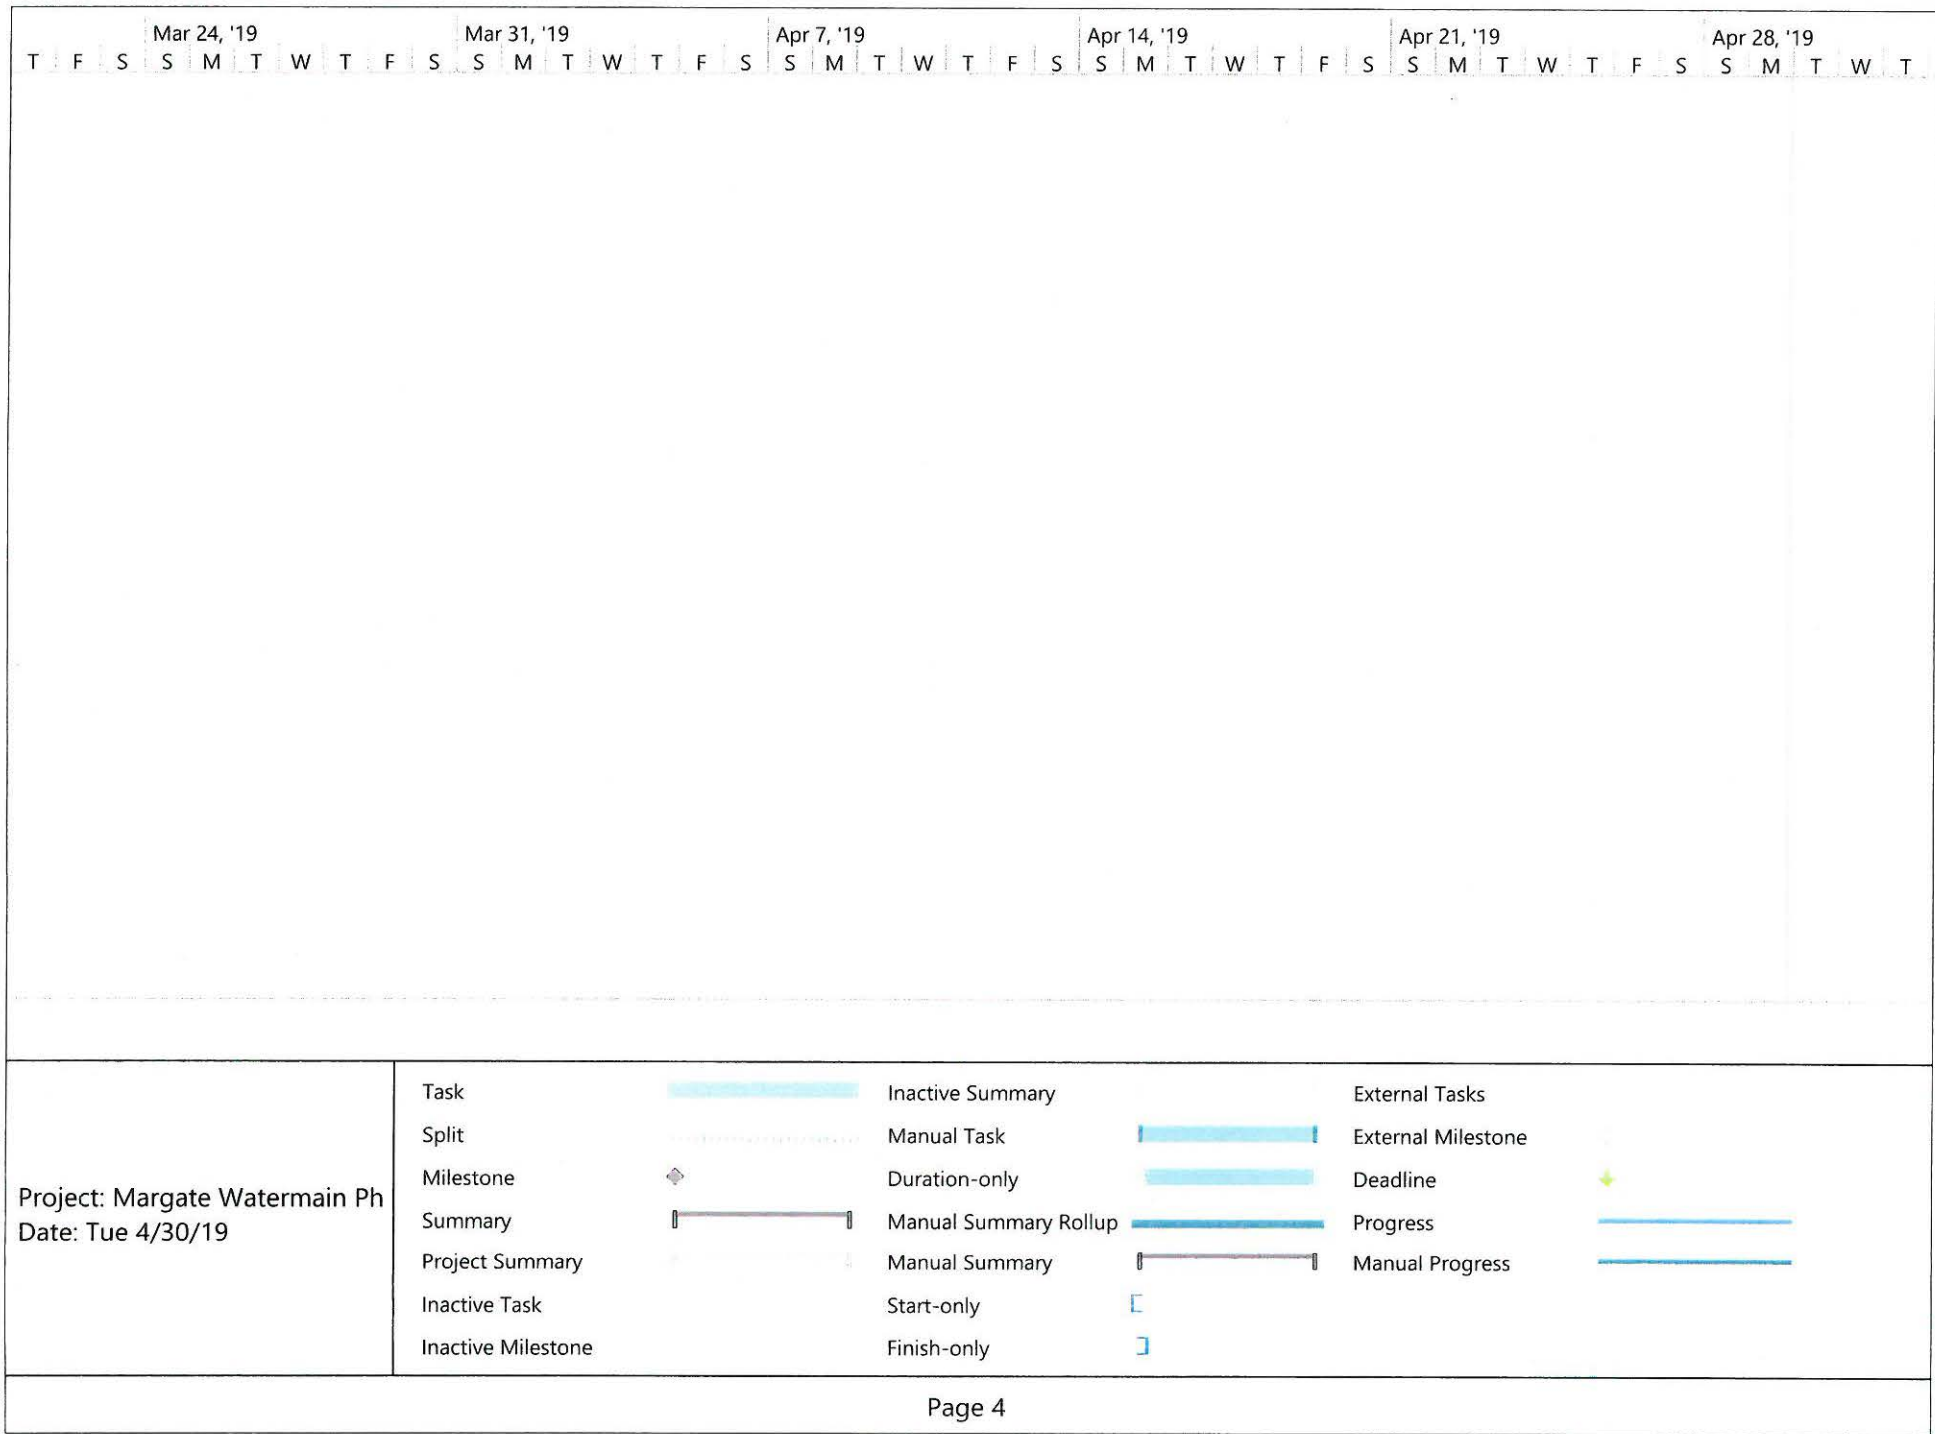












Project: Margate Watermain Ph Date: Tue 4/30/19	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			


ID		Task Mode	Task Name	Duration	Start	Finish	% Complete	Mar 17, '19								
								W	T	F	S	S	M	T	W	T
30			Phase 10 Crew 2 - Services & Restoration	10 days	Wed 12/11/19	Thu 12/26/19	0%									
31			Phase 11 Crew 1 - Pipe Installation	10 days	Fri 12/27/19	Mon 1/13/20	0%									
32			Phase 11 Crew 2 - Services & Restoration	10 days	Fri 12/27/19	Mon 1/13/20	0%									
33							0%									
34			Testing & Closeout	28 days	Tue 1/14/20	Thu 2/20/20	0%									
35			Site Restoration	14 days	Tue 1/14/20	Fri 1/31/20	0%									
36			Substantial Completion	1 day	Tue 1/14/20	Tue 1/14/20	0%									
37			Pressure Testing	5 days	Tue 1/21/20	Mon 1/27/20	0%									
38			Bacteriological Testing	5 days	Tue 1/21/20	Mon 1/27/20	0%									
39			Record Drawings	10 days	Tue 1/21/20	Mon 2/3/20	0%									
40			Clean up & Final Completion	9 days	Mon 1/27/20	Thu 2/6/20	0%									

Project: Margate Watermain Ph Date: Tue 4/30/19	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			




			Mar 24, '19							Mar 31, '19							Apr 7, '19							Apr 14, '19							Apr 21, '19							Apr 28, '19						
T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T									

Project: Margate Watermain Ph Date: Tue 4/30/19	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

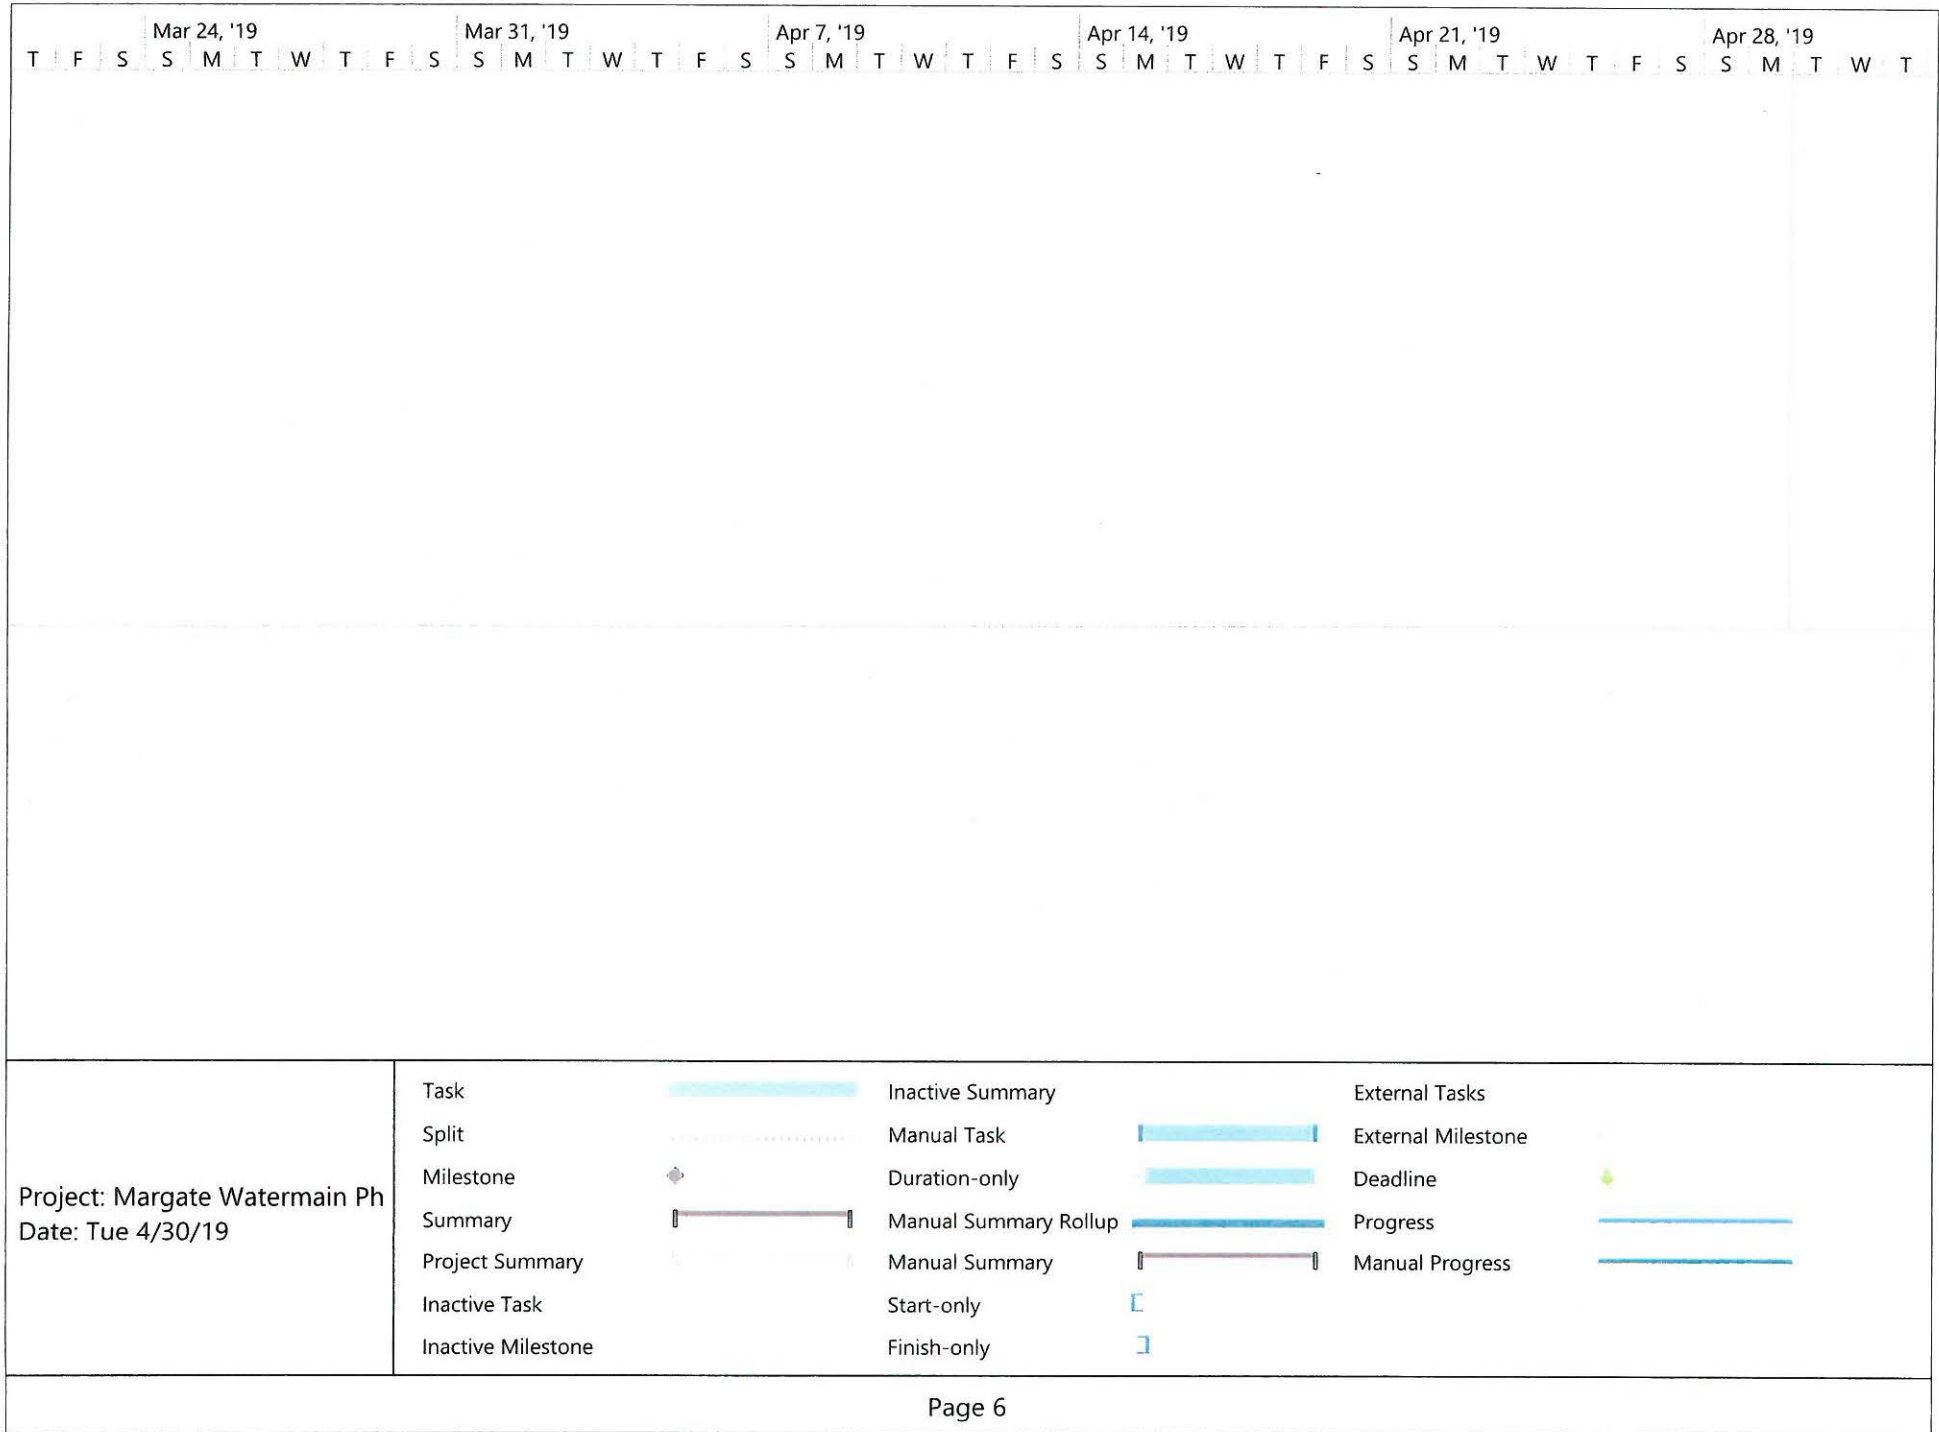

May 5, '19							May 12, '19							May 19, '19							May 26, '19							Jun 2, '19							Jun 9, '19							
F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F

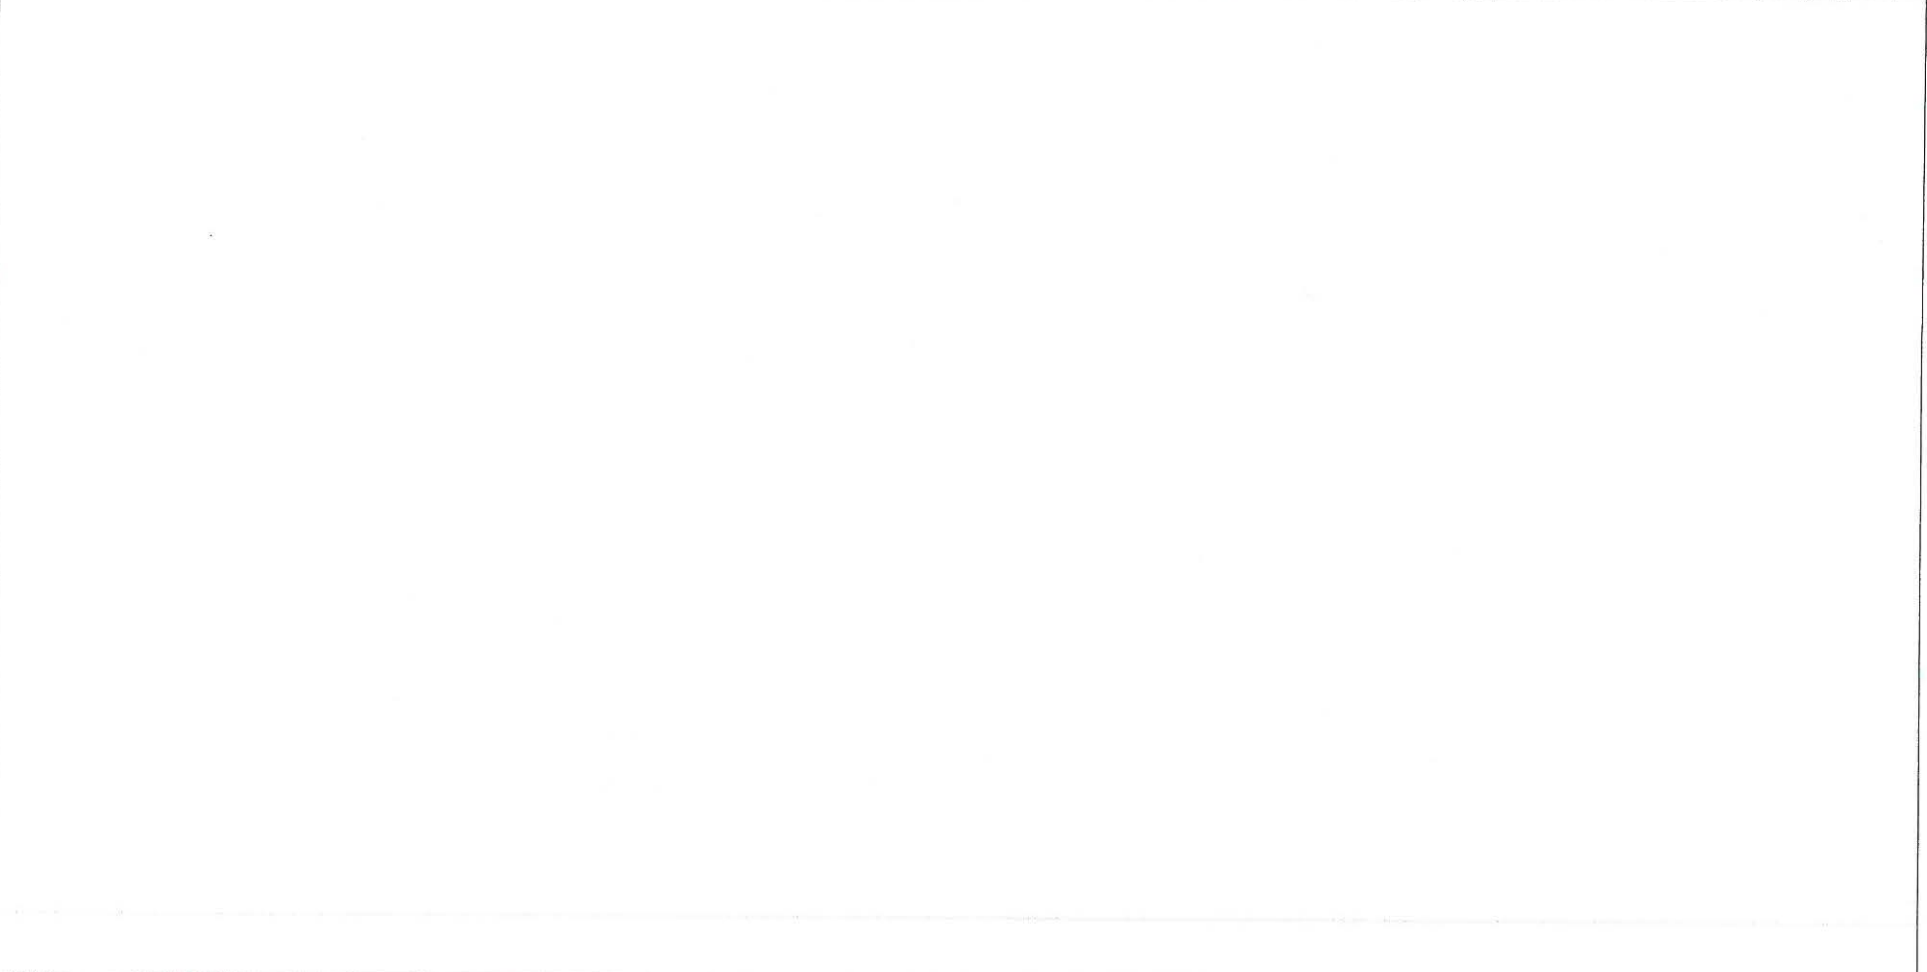

Project: Margate Watermain Ph Date: Tue 4/30/19	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

May 5, '19							May 12, '19							May 19, '19							May 26, '19							Jun 2, '19							Jun 9, '19						
F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	F	S	S	M	T	W	T	F	S	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F		

Project: Margate Watermain Ph
Date: Tue 4/30/19

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone



Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only




External Tasks

External Milestone

Deadline

Progress

Manual Progress



May 5, '19							May 12, '19							May 19, '19							May 26, '19							Jun 2, '19							Jun 9, '19						
F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S					

Project: Margate Watermain Ph
Date: Tue 4/30/19

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only


External Tasks

External Milestone


Deadline

Progress

Manual Progress

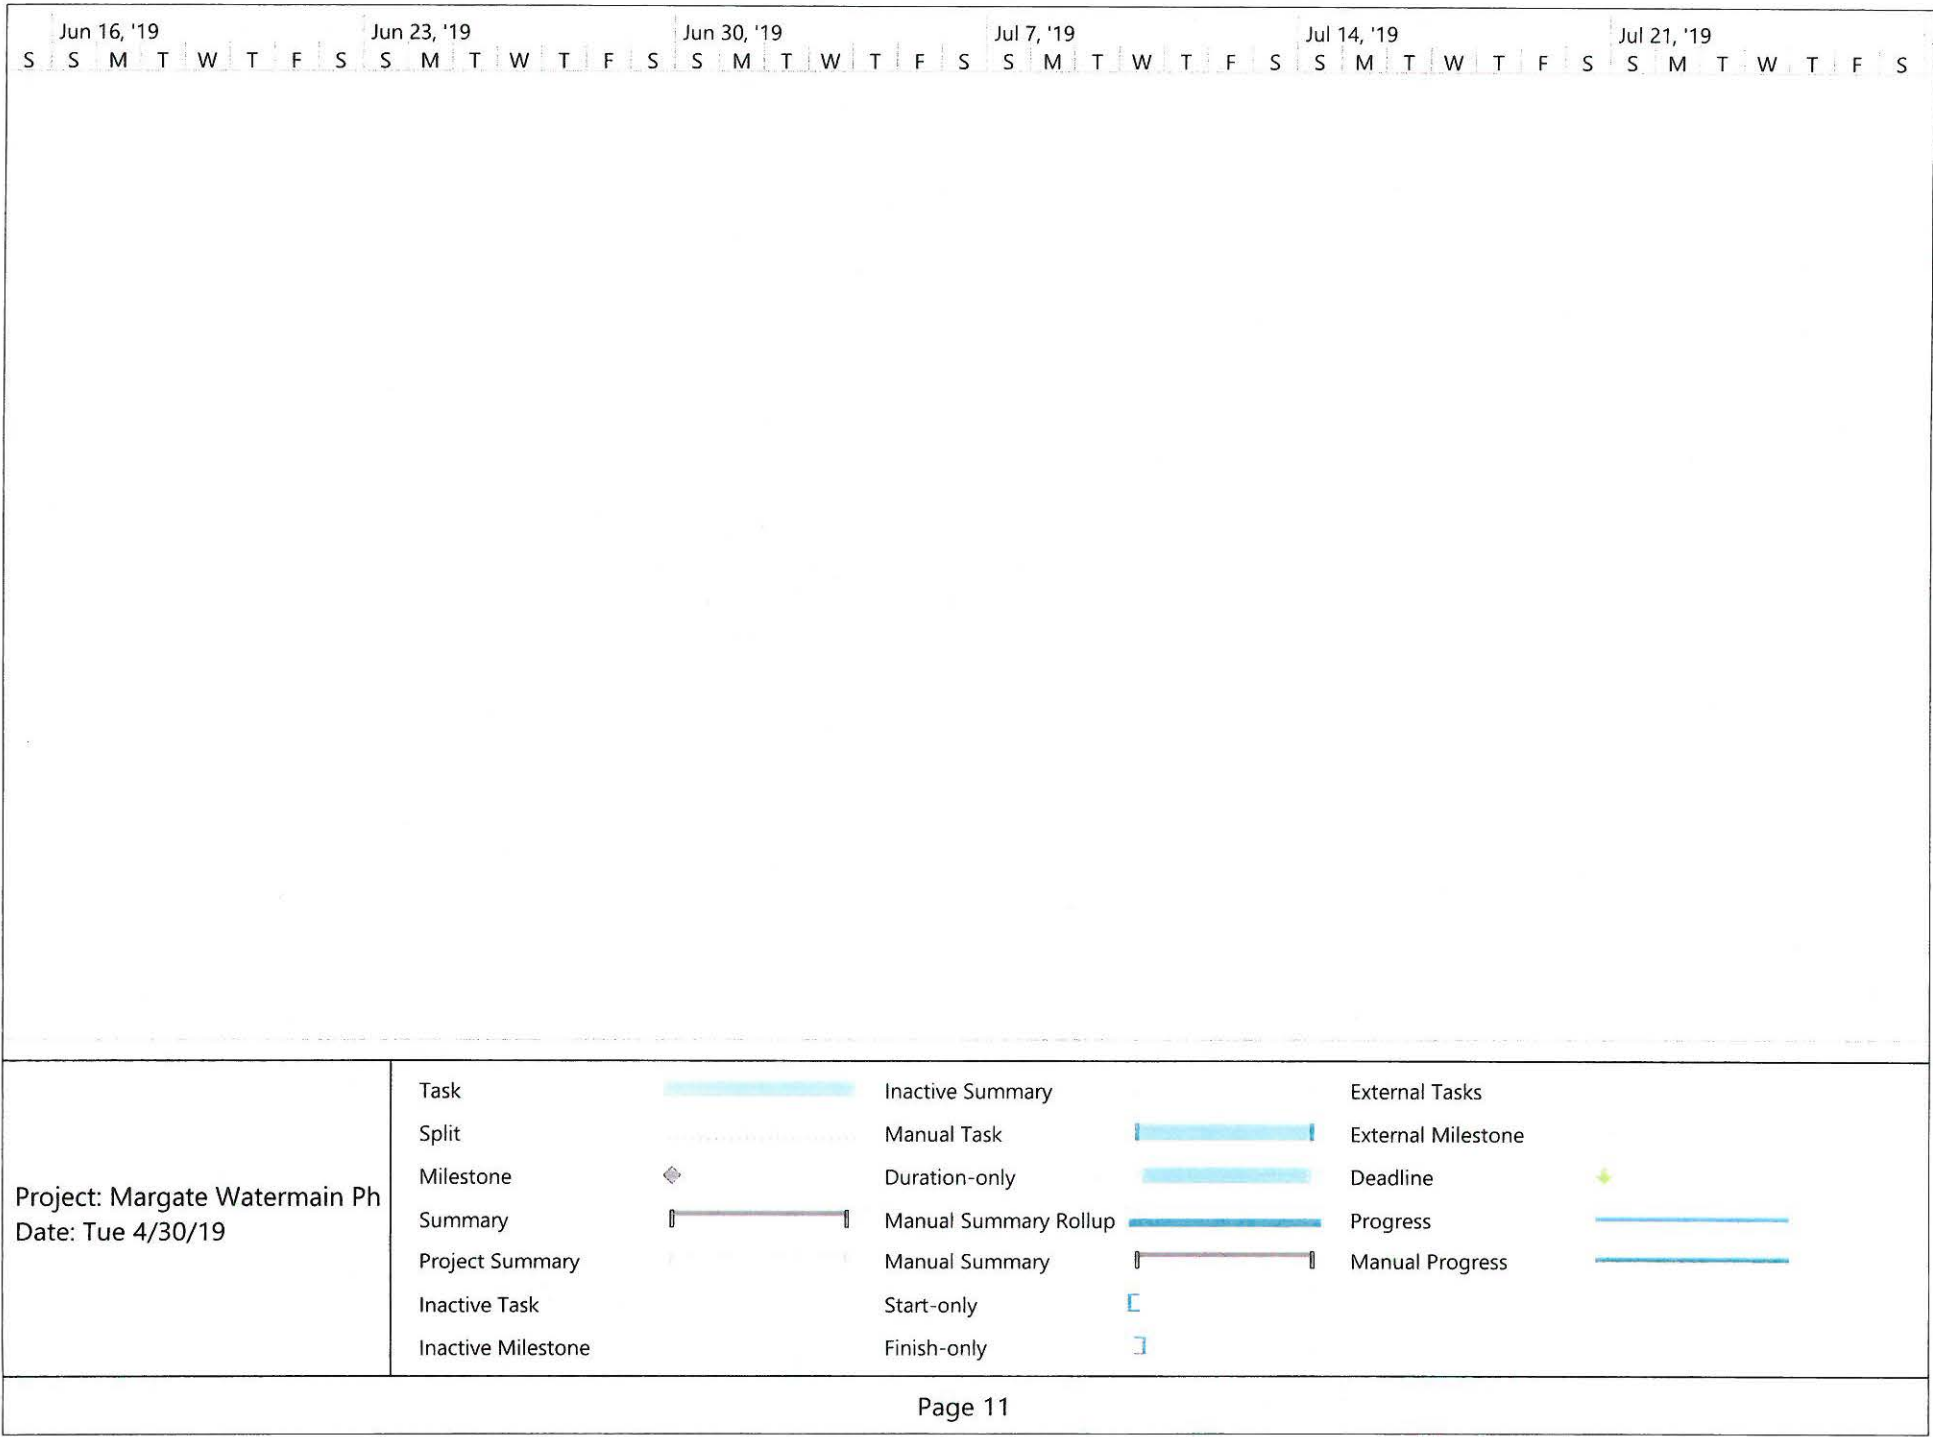


Jun 16, '19							Jun 23, '19							Jun 30, '19							Jul 7, '19							Jul 14, '19							Jul 21, '19						
S	S	M	T	W	T	F	S	S	S	M	T	W	T	F	S	S	S	M	T	W	T	F	S	S	S	M	T	W	T	F	S	S	S	M	T	W	T	F	S		

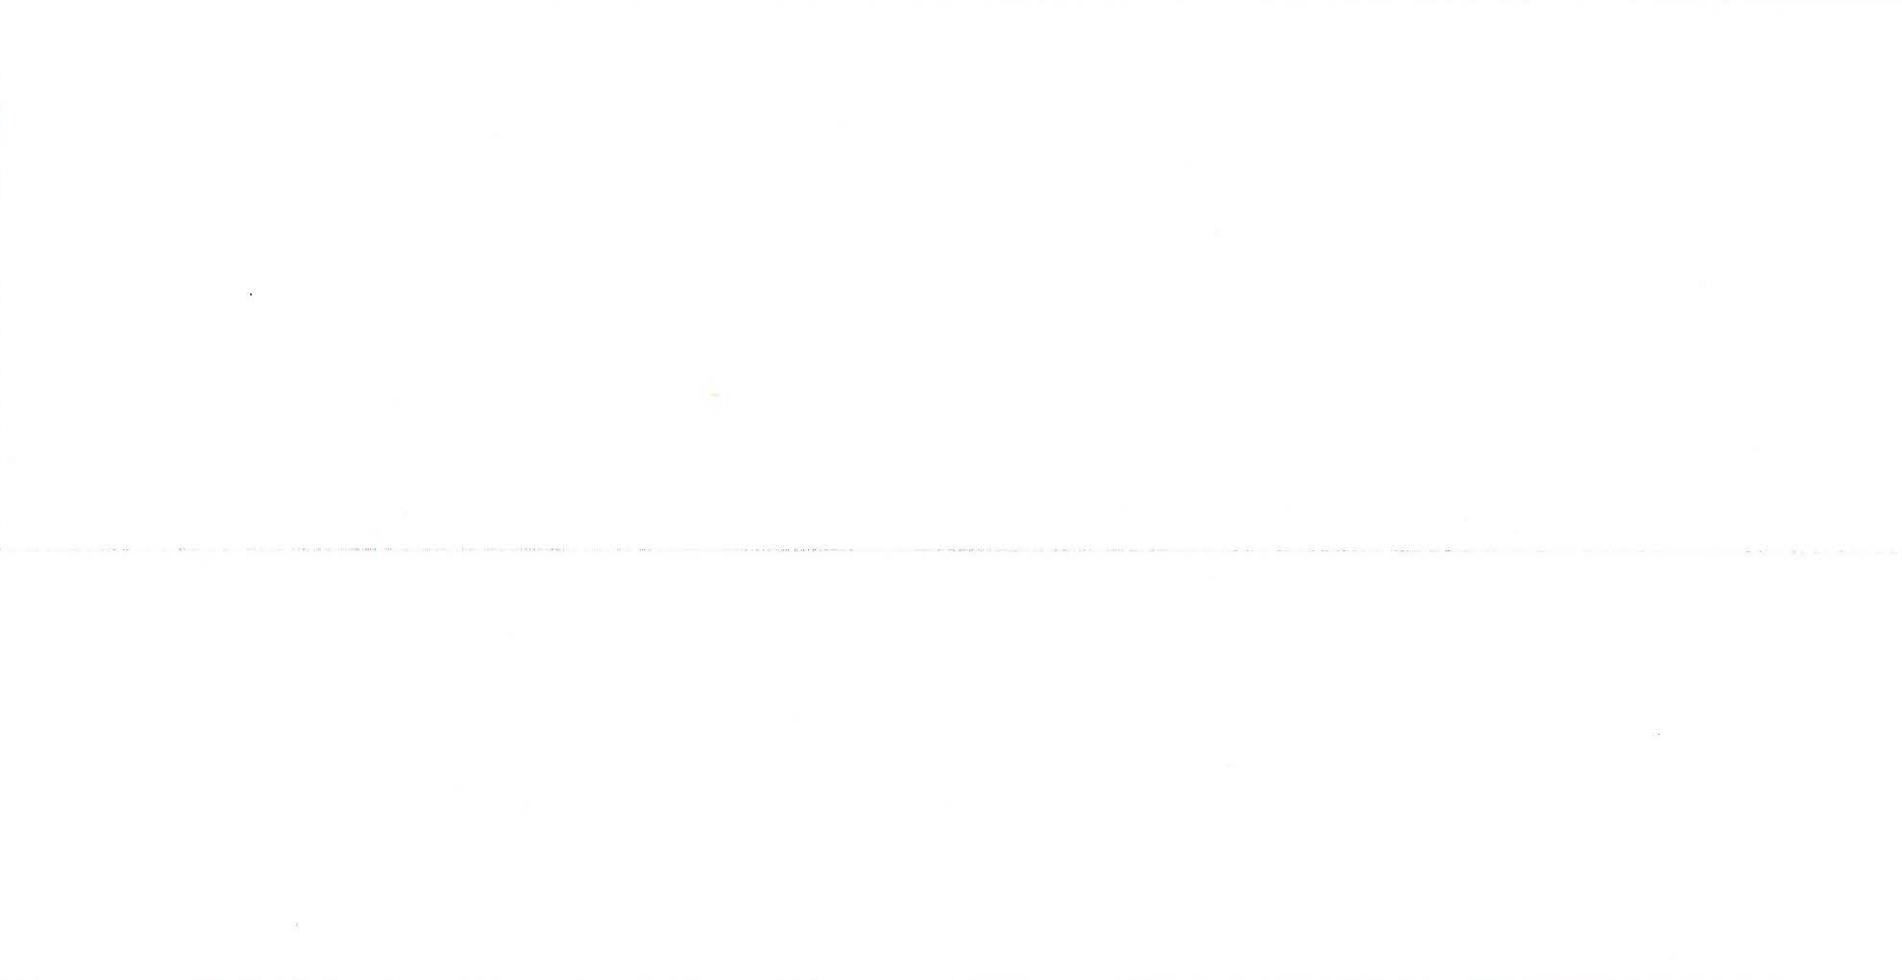

Project: Margate Watermain Ph Date: Tue 4/30/19	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

Jul 28, '19 Aug 4, '19 Aug 11, '19 Aug 18, '19 Aug 25, '19 Sep 1, '19 Sep 8, '19

S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S

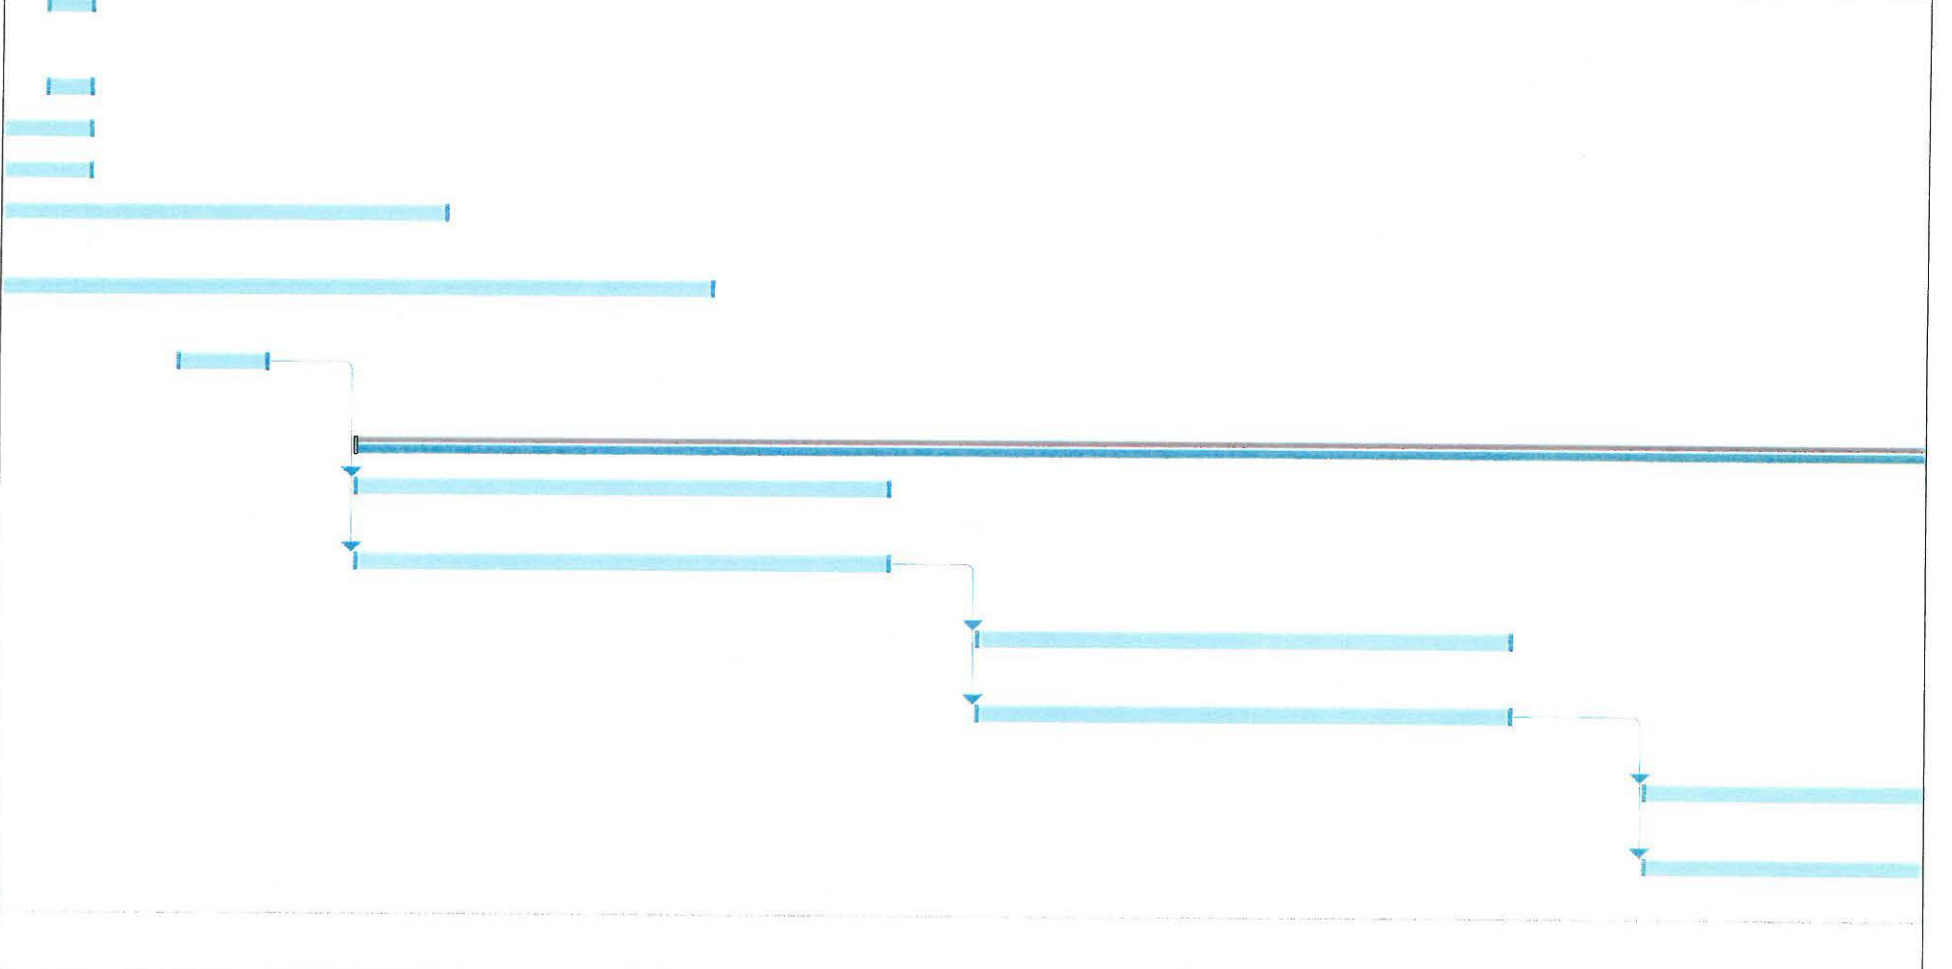

Project: Margate Watermain Ph
Date: Tue 4/30/19

Jul 28, '19 Aug 4, '19 Aug 11, '19 Aug 18, '19 Aug 25, '19 Sep 1, '19 Sep 8, '19

S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S

Project: Margate Watermain Ph
Date: Tue 4/30/19

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone



Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only



External Tasks

External Milestone

Deadline
















Progress

Manual Progress

















Jul 28, '19 S M T W T F S
 Aug 4, '19 S M T W T F S
 Aug 11, '19 S M T W T F S
 Aug 18, '19 S M T W T F S
 Aug 25, '19 S M T W T F S
 Sep 1, '19 S M T W T F S
 Sep 8, '19 S

Project: Margate Watermain Ph
 Date: Tue 4/30/19

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			















8, '19	Sep 15, '19							Sep 22, '19							Sep 29, '19							Oct 6, '19							Oct 13, '19							Oct 20, '1		
M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M			






















Project: Margate Watermain Ph Date: Tue 4/30/19	Task		Inactive Summary		External Tasks
	Split		Manual Task		External Milestone
	Milestone		Duration-only		Deadline
	Summary		Manual Summary Rollup		Progress
	Project Summary		Manual Summary		Manual Progress
	Inactive Task		Start-only		
	Inactive Milestone		Finish-only		

8, '19							Sep 15, '19							Sep 22, '19							Sep 29, '19							Oct 6, '19							Oct 13, '19							Oct 20, '1		
M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M		

Project: Margate Watermain Ph
Date: Tue 4/30/19

Task		Inactive Summary		External Tasks
Split		Manual Task		External Milestone
Milestone		Duration-only		Deadline
Summary		Manual Summary Rollup		Progress
Project Summary		Manual Summary		Manual Progress
Inactive Task		Start-only		
Inactive Milestone		Finish-only		

<div>Project: Margate Watermain Ph</div> <div>Date: Tue 4/30/19</div>	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

19

Oct 27, '19

Nov 3, '19

Nov 10, '19

Nov 17, '19

Nov 24, '19

Dec 1, '19

T

W

T

F

S

S

M

T

W

T

F

S

S

M

T

W

T

F

S

S

M

T

W

T

F

S

S

M

T

W

T

F

S

S

M

T

W

T

F

S

S

M

T

Project: Margate Watermain Ph

Date: Tue 4/30/19

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

Manual Progress

Dec 8, '19
 W T F S S M T W T F S
 Dec 15, '19
 S M T W T F S
 Dec 22, '19
 S M T W T F S
 Dec 29, '19
 S M T W T F S
 Jan 5, '20
 S M T W T F S
 Jan 12, '20
 S M T W



Project: Margate Watermain Ph
 Date: Tue 4/30/19


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

W T F S Dec 8, '19 S M T W T F S Dec 15, '19 S M T W T F S Dec 22, '19 S M T W T F S Dec 29, '19 S M T W T F S Jan 5, '20 S M T W T F S Jan 12, '20 S M T W




Project: Margate Watermain Ph Date: Tue 4/30/19	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W
 Dec 8, '19 Dec 15, '19 Dec 22, '19 Dec 29, '19 Jan 5, '20 Jan 12, '20

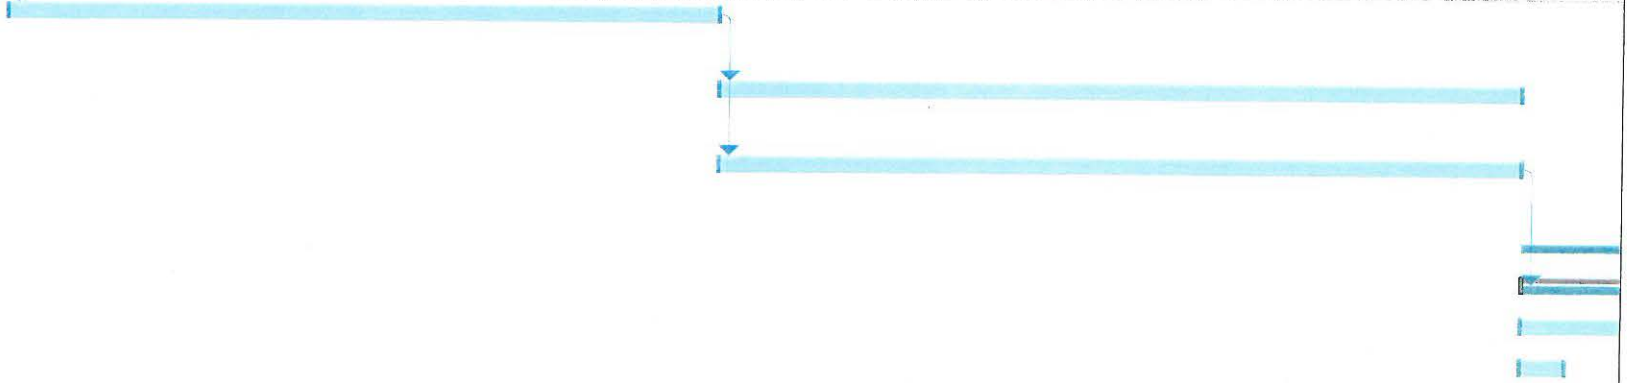

Project: Margate Watermain Ph
 Date: Tue 4/30/19


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

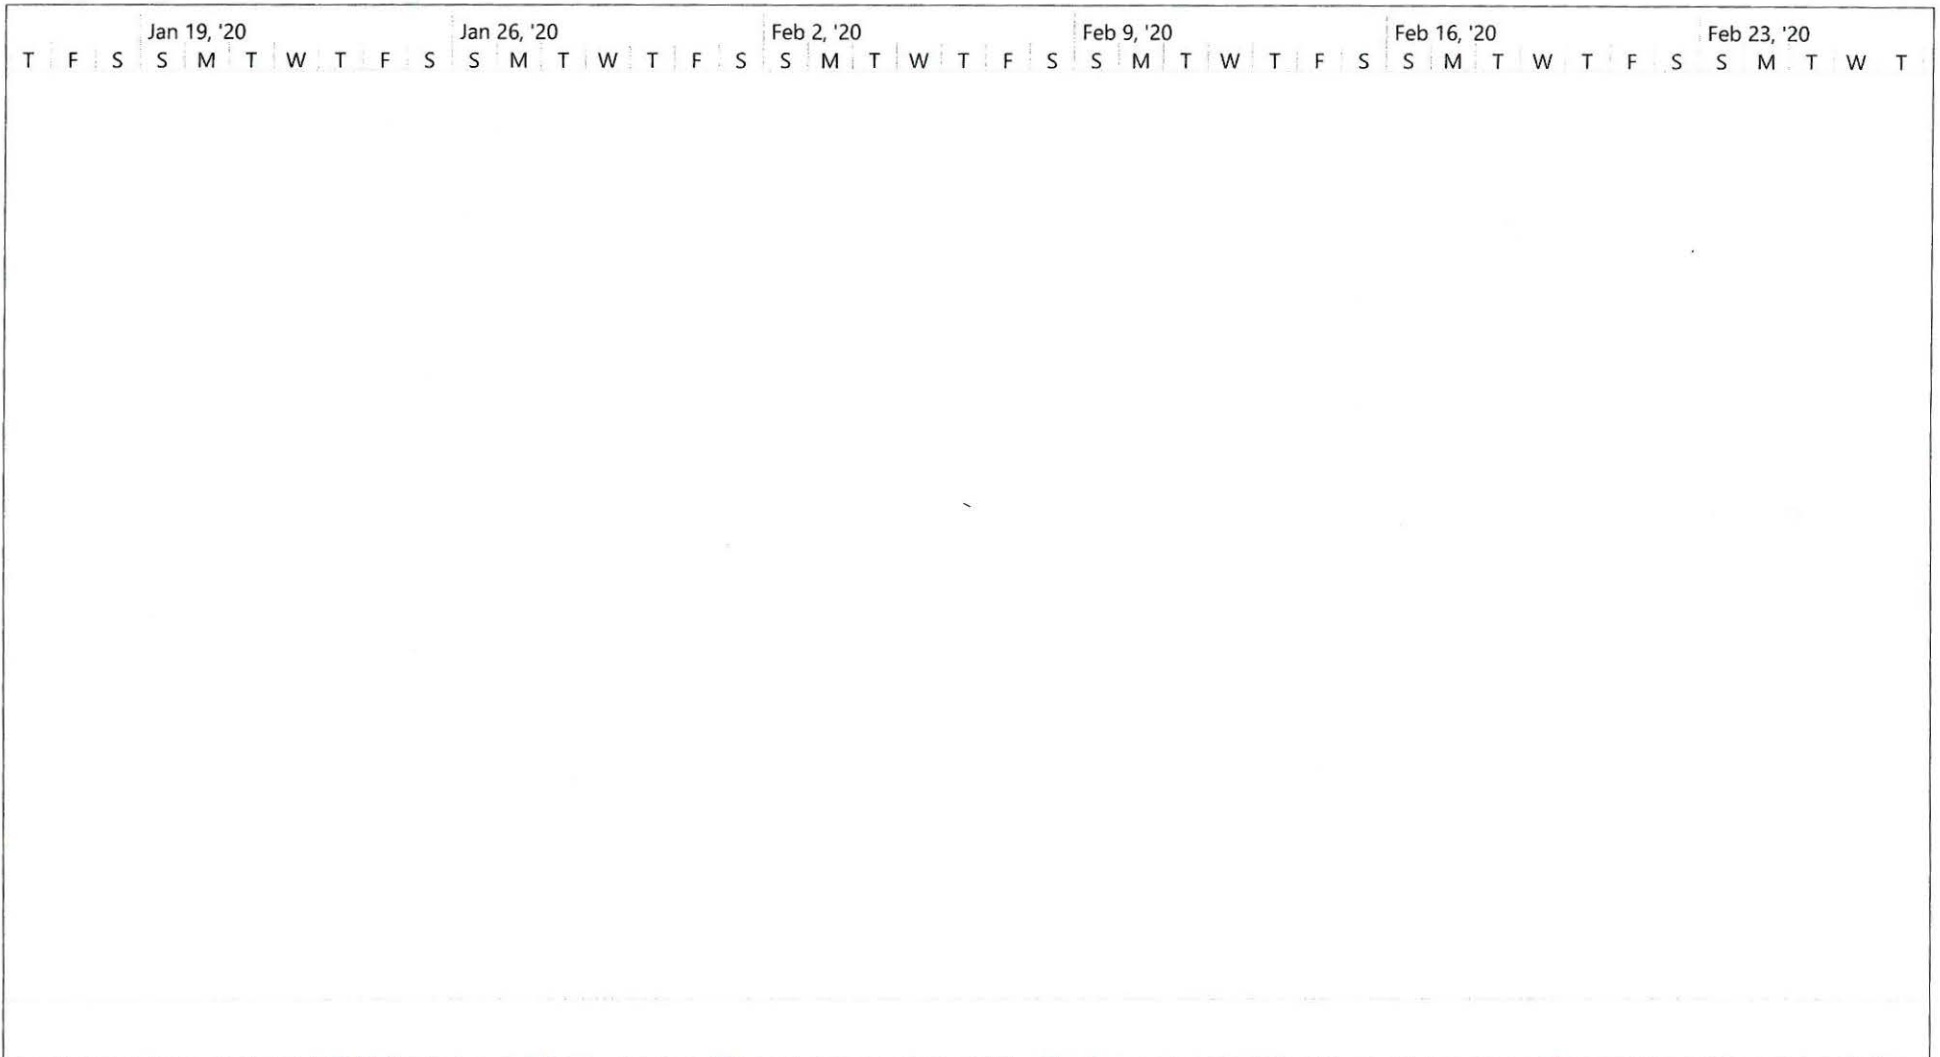

Project: Margate Watermain Ph Date: Tue 4/30/19	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



Project: Margate Watermain Ph Date: Tue 4/30/19	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

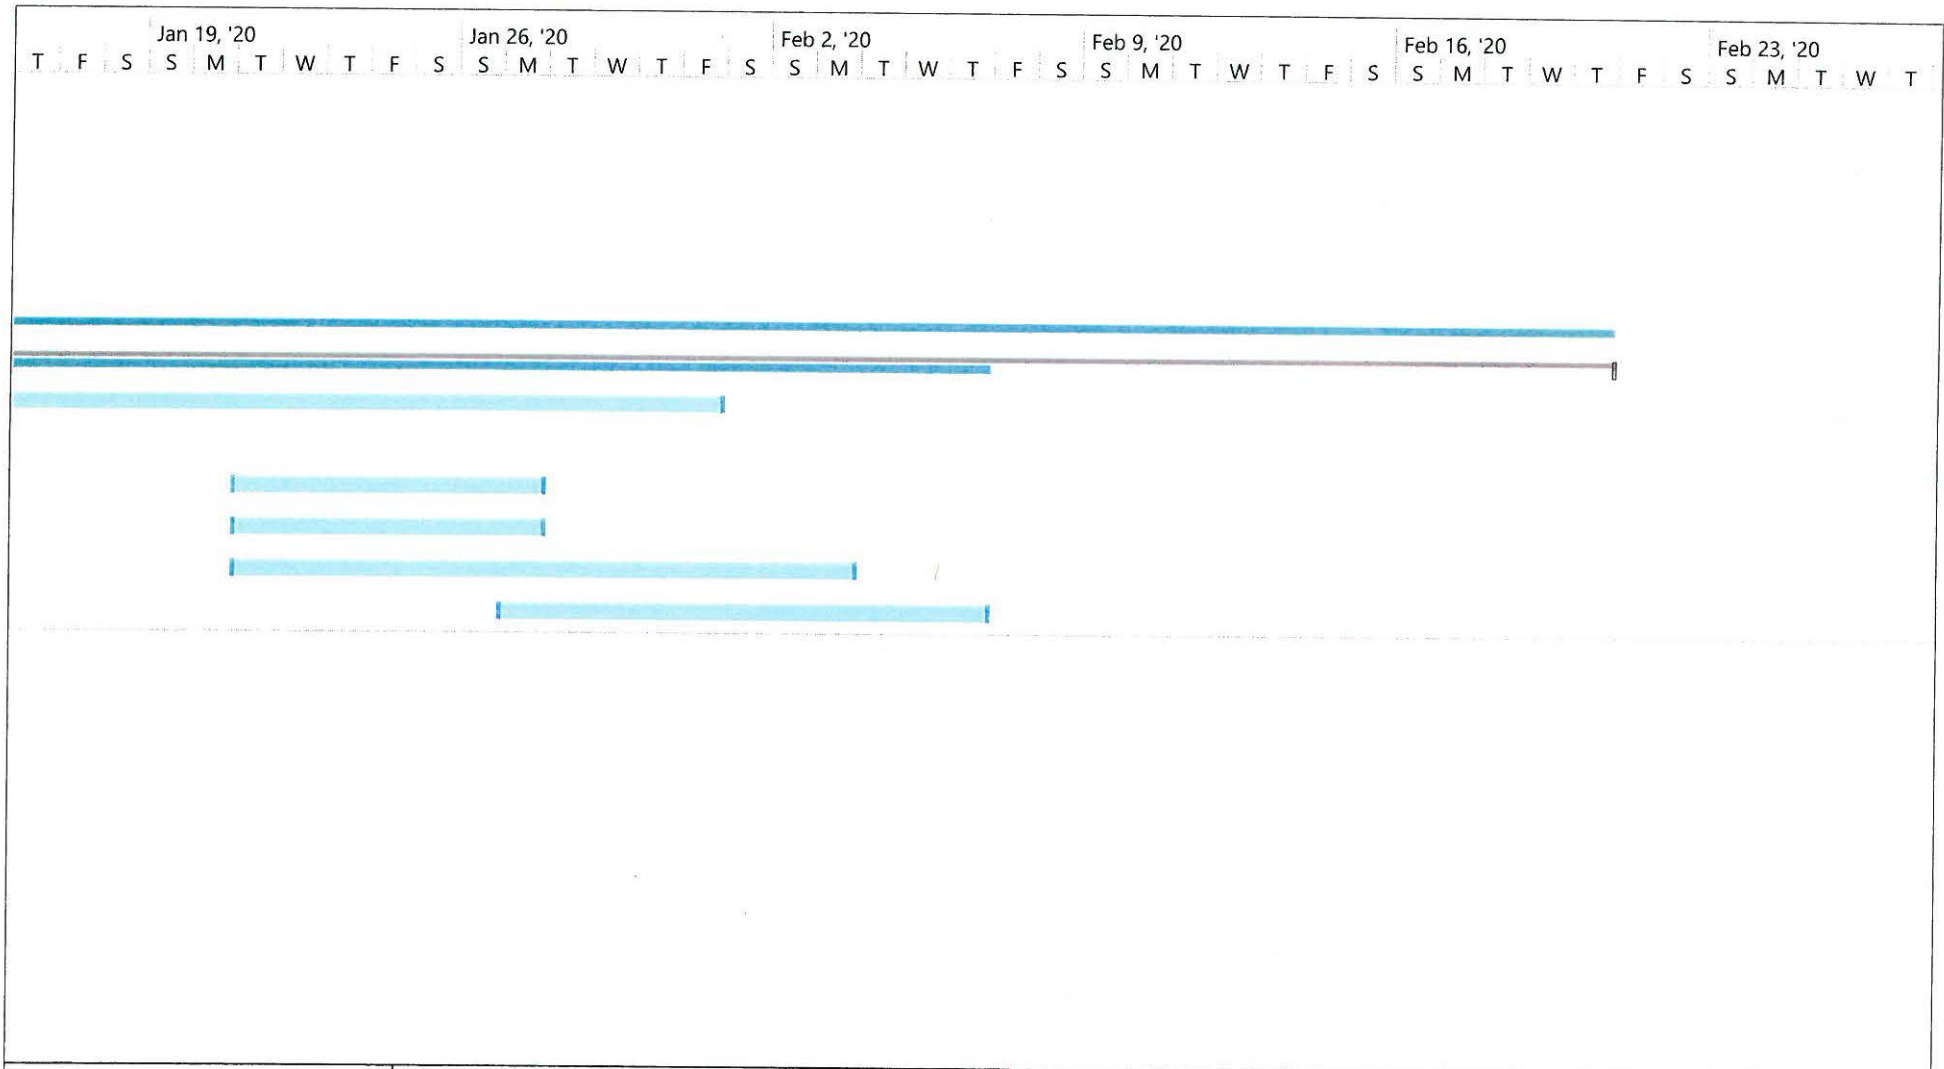

Project: Margate Watermain Ph Date: Tue 4/30/19	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



RICK SCOTT, GOVERNOR

JONATHAN ZACHEM, SECRETARY



STATE OF FLORIDA
DEPARTMENT OF BUSINESS AND PROFESSIONAL REGULATION
CONSTRUCTION INDUSTRY LICENSING BOARD

THE GENERAL CONTRACTOR HEREIN IS CERTIFIED UNDER THE
PROVISIONS OF CHAPTER 489, FLORIDA STATUTES

LYSSENKO, ILIA V

DBF CONSTRUCTION LLC
2660 NW 15TH CT SUITE 108
POMPANO BEACH FL 33069

LICENSE NUMBER: CGC1512467

EXPIRATION DATE: AUGUST 31, 2020

Always verify licenses online at MyFloridaLicense.com



Do not alter this document in any form.

This is your license. It is unlawful for anyone other than the licensee to use this document.



RICK SCOTT, GOVERNOR

JONATHAN ZACHEM, SECRETARY



STATE OF FLORIDA
DEPARTMENT OF BUSINESS AND PROFESSIONAL REGULATION
CONSTRUCTION INDUSTRY LICENSING BOARD

THE UNDERGROUND UTILITY & EXCAVATION CO HEREIN IS CERTIFIED UNDER THE
PROVISIONS OF CHAPTER 489, FLORIDA STATUTES

LYSENKO, ILIA V

DBF CONSTRUCTION LLC
268 NW 118 DRIVE
CORAL SPRINGS FL 33071

LICENSE NUMBER: CUC1224328

EXPIRATION DATE: AUGUST 31, 2020

Always verify licenses online at MyFloridaLicense.com



Do not alter this document in any form.

This is your license. It is unlawful for anyone other than the licensee to use this document.

Client#: 6898

DBFCO

ACORD™

CERTIFICATE OF LIABILITY INSURANCE

DATE (MM/DD/YYYY)

08/20/2018

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AFFIRMATIVELY OR NEGATIVELY AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW. THIS CERTIFICATE OF INSURANCE DOES NOT CONSTITUTE A CONTRACT BETWEEN THE ISSUING INSURER(S), AUTHORIZED REPRESENTATIVE OR PRODUCER, AND THE CERTIFICATE HOLDER.

IMPORTANT: If the certificate holder is an ADDITIONAL INSURED, the policy(ies) must be endorsed. If SUBROGATION IS WAIVED, subject to the terms and conditions of the policy, certain policies may require an endorsement. A statement on this certificate does not confer rights to the certificate holder in lieu of such endorsement(s).

PRODUCER ZERVOS GROUP, INC. 24724 Farmbrook P.O. Box 2067 Southfield, MI 48037-2067		CONTACT NAME: PHONE (A/C, No, Ext): 248 355-4411 FAX (A/C, No): 248 355-2175 E-MAIL ADDRESS:	
INSURED DBF CONSTRUCTION, LLC 1850 NW 15th Ave. Suite 225 Pompano Beach, FL 33069		INSURER(S) AFFORDING COVERAGE INSURER A : National Trust Insurance Company INSURER B : FCCI Insurance Company INSURER C : INSURER D : INSURER E : INSURER F :	

COVERAGES

CERTIFICATE NUMBER:

REVISION NUMBER:

THIS IS TO CERTIFY THAT THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATION MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.

INSR LTR	TYPE OF INSURANCE	ADDL SUBR INSR WVD	POLICY NUMBER	POLICY EFF (MM/DD/YYYY)	POLICY EXP (MM/DD/YYYY)	LIMITS
A	<input checked="" type="checkbox"/> COMMERCIAL GENERAL LIABILITY <input type="checkbox"/> CLAIMS-MADE <input checked="" type="checkbox"/> OCCUR <input checked="" type="checkbox"/> PD Ded:1,000 GEN'L AGGREGATE LIMIT APPLIES PER: <input type="checkbox"/> POLICY <input type="checkbox"/> PRO-JECT <input type="checkbox"/> LOC OTHER:		CPP0020970	08/10/2018	08/10/2019	EACH OCCURRENCE \$1,000,000 DAMAGE TO RENTED PREMISES (Ea occurrence) \$100,000 MED EXP (Any one person) \$5,000 PERSONAL & ADV INJURY \$1,000,000 GENERAL AGGREGATE \$2,000,000 PRODUCTS - COMP/OP AGG \$2,000,000 \$
B	AUTOMOBILE LIABILITY <input checked="" type="checkbox"/> ANY AUTO <input type="checkbox"/> ALL OWNED AUTOS <input checked="" type="checkbox"/> HIRED AUTOS <input checked="" type="checkbox"/> SCHEDULED AUTOS NON-OWNED AUTOS <input checked="" type="checkbox"/> Drive Oth Car		CA100005281	08/10/2018	08/10/2019	COMBINED SINGLE LIMIT (Ea accident) \$1,000,000 BODILY INJURY (Per person) \$ BODILY INJURY (Per accident) \$ PROPERTY DAMAGE (Per accident) \$ \$
B	<input checked="" type="checkbox"/> UMBRELLA LIAB <input checked="" type="checkbox"/> OCCUR <input type="checkbox"/> EXCESS LIAB <input type="checkbox"/> CLAIMS-MADE DED <input checked="" type="checkbox"/> RETENTION \$0		UMB0021714	08/10/2018	08/10/2019	EACH OCCURRENCE \$2,000,000 AGGREGATE \$2,000,000 \$
B	WORKERS COMPENSATION AND EMPLOYERS' LIABILITY ANY PROPRIETOR/PARTNER/EXECUTIVE OFFICER/MEMBER EXCLUDED? <input checked="" type="checkbox"/> Y/N <input checked="" type="checkbox"/> N/A (Mandatory in NH) If yes, describe under DESCRIPTION OF OPERATIONS below		001WC17A73980	08/10/2018	08/10/2019	<input checked="" type="checkbox"/> PER STATUTE <input type="checkbox"/> OTH-ER E.L. EACH ACCIDENT \$1,000,000 E.L. DISEASE - EA EMPLOYEE \$1,000,000 E.L. DISEASE - POLICY LIMIT \$1,000,000
A	Leased or Rented Equipment Scheduled Equip.		CPP0020970	08/10/2018	08/10/2019	\$100,000 Limit \$500 Deductible Limit/Ded. shown below

DESCRIPTION OF OPERATIONS / LOCATIONS / VEHICLES (ACORD 101, Additional Remarks Schedule, may be attached if more space is required)

Illustration of coverage only.

CERTIFICATE HOLDER

CANCELLATION

ILLUSTRATION OF COVERAGE ONLY

SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, NOTICE WILL BE DELIVERED IN ACCORDANCE WITH THE POLICY PROVISIONS.

AUTHORIZED REPRESENTATIVE

Ch. B. Jones

© 1988-2014 ACORD CORPORATION. All rights reserved.

BROWARD COUNTY LOCAL BUSINESS TAX RECEIPT

115 S. Andrews Ave., Rm. A-100, Ft. Lauderdale, FL 33301-1895 – 954-831-4000

VALID OCTOBER 1, 2018 THROUGH SEPTEMBER 30, 2019

DBA: DBF CONSTRUCTION LLC
Business Name: DBF CONSTRUCTION LLC

Receipt #: 180-258258
Business Type: GENERAL CONTRACTOR (GENERAL CONTRACTOR)

Owner Name: ILIA V LYSSENKO
Business Location: 1850 NW 15TH AVE
POMPANO BEACH
Business Phone: 954-892-1697

Business Opened: 10/09/2013
State/County/Cert/Reg: CGC1512467
Exemption Code:

Rooms **Seats** **Employees** **Machines** **Professionals**
8

For Vending Business Only						
Number of Machines:				Vending Type:		
Tax Amount	Transfer Fee	NSF Fee	Penalty	Prior Years	Collection Cost	Total Paid
27.00	0.00	0.00	0.00	0.00	0.00	27.00

THIS RECEIPT MUST BE POSTED CONSPICUOUSLY IN YOUR PLACE OF BUSINESS

THIS BECOMES A TAX RECEIPT

WHEN VALIDATED

This tax is levied for the privilege of doing business within Broward County and is non-regulatory in nature. You must meet all County and/or Municipality planning and zoning requirements. This Business Tax Receipt must be transferred when the business is sold, business name has changed or you have moved the business location. This receipt does not indicate that the business is legal or that it is in compliance with State or local laws and regulations.

Mailing Address:

DBF CONSTRUCTION LLC
1850 NW 15TH AVE
SUITE 225
POMPANO BEACH, FL 33069

Receipt # 1CP-17-00013634
Paid 07/16/2018 27.00

2018 - 2019



**CITY OF POMPAÑO BEACH
BUSINESS TAX RECEIPT
FISCAL YEAR: 2018 - 2019**

THIS IS NOT A BILL

Business Tax Receipt Valid from: October 1, 2018 through September 30, 2019

10/3/2018

4457226
DBF CONSTRUCTION LLC
MARK GIANNETTI
6044 NW 74 TERRACE
CORAL SPRINGS FL 33067

THIS IS YOUR BUSINESS TAX RECEIPT. PLEASE POST IN A CONSPICUOUS PLACE AT THE BUSINESS LOCATION.

BUSINESS OWNER: DBF CONSTRUCTION LLC
BUSINESS LOCATION: 1850 NW 15 AV 225 POMPAÑO BEACH FL

RECEIPT NO:	CLASSIFICATION
19-00083704	CONTRACTOR GENERAL (GC)

NOTICE: A NEW APPLICATION MUST BE FILED IF THE BUSINESS NAME, OWNERSHIP OR ADDRESS IS CHANGED. THE ISSUANCE OF A BUSINESS TAX RECEIPT SHALL NOT BE DEEMED A WAIVER OF ANY PROVISION OF THE CITY CODE NOR SHALL THE ISSUANCE OF A BUSINESS TAX RECEIPT BE CONSTRUED TO BE A JUDGEMENT OF THE CITY AS TO THE COMPETENCE OF THE APPLICANT TO TRANSACT BUSINESS. **THIS DOCUMENT CANNOT BE ALTERED.**

BUSINESS TAX RECEIPTS EXPIRE SEPTEMBER 30TH OF EACH YEAR

State of Florida

Department of State

I certify from the records of this office that DBF CONSTRUCTION LLC is a limited liability company organized under the laws of the State of Florida, filed on July 3, 2013, effective July 3, 2013.

The document number of this limited liability company is L13000095337.

I further certify that said limited liability company has paid all fees due this office through December 31, 2019, that its most recent annual report was filed on February 6, 2019, and that its status is active.

*Given under my hand and the
Great Seal of the State of Florida
at Tallahassee, the Capital, this
the Sixth day of February, 2019*



Randy Be
Secretary of State

Tracking Number: 0101327844CC

To authenticate this certificate, visit the following site, enter this number, and then follow the instructions displayed.

<https://services.sunbiz.org/Filings/CertificateOfStatus/CertificateAuthentication>

CHRISTOPHER J. IACOBELLI

CHRIS@DBFCONST.COMCAS
TBIZ.NET

954-892-0678



LINKEDIN URL

LINK TO OTHER ONLINE
PROPERTIES:
PORTFOLIO/WEBSITE/BLOG

OBJECTIVE

To get started, click placeholder
text and start typing. Be brief:
one or two sentences.

SKILLS

Explain what you're especially
good at. What sets you apart?
Use your own language—not
jargon.

EXPERIENCE

Equipment operator / Foreman / Superintendent / Project Manager / Estimator

Dates From 1982 to 1990

Iacobelli Contracting, Inc.

Medley, Florida

Performed multiple tasks on large diameter transmission mains for
Miami Dade Water & Sewer Authority

Tasks included:

- Planning laying schedules
- Coordinating crews for installation, cleaning, joint welding,
testing, & restoration

Also oversaw all heavy equipment maintenance and repair

OWNER / PRESIDENT OF COASTAL UTILITIES, INC. COOPER CITY, FL.

Dates From 1990 - 1997

Completed approximately \$30 million of Water Main, Sanitary
Sewer, & Storm Drainage Improvements in the Dade, Broward, Palm
Beach, & Monroe Counties

Project Manager / Estimator

Megan South, LLC

Davie, FL.

Dates From 1997 - 2001

Completed approximately \$10 million of
Earthwork, Water Main, Sanitary Sewer, Storm Drainage, &
Roadway construction within Dade, Broward, Palm Beach, & Monroe
Counties

Part Owner / Estimator / Project Manager

Dates from 2016 - 2018

Oversaw multiple crews and subcontractors on the Hard Rock Stadium Site Improvements Project including Demolition, Water Main, Storm Drainage, Sanitary Sewer, Textured Concrete, Brick Pavers, Curb & Gutter, Parking Lot Reconstruction, Striping / Signage, & Landscaping,

Also oversaw the scheduling, Inspection, material requirements, equipment allocation, and manpower allocation for multiple Road Building crews on a Neighborhood Improvement project in Davie, Fl.

Project Manager and Field Superintendent

DBF Construction, LLC

Dates from 2018 – Current

Oversee multiple crews on several Water Main, Sanitary Sewer, Storm Drainage, & Water Reuse projects

EDUCATION

DEGREE / DATE EARNED

School
Bachelor of Arts
Florida Atlantic University
1982

VOLUNTEER EXPERIENCE OR LEADERSHIP
